

INSTALLATION SEQUENCE

HC PRECAST SYSTEM

IBS Superstructure In Malaysia 3 in 1

Load Bearing Wall + Modular Shear Keys Wet Joint + Box System

- Speed, Quality & Environment




- The wall is designed to provide adequate fire resistance according to demand (with minimum 2hours as per BS8110)
- The system is designed and approved by PE and endorsed by independent checker
- Thickness of the wall can be customized according to requirement
- Our design and casting are following strictly to British Standard

INDUSTRIALISED BUILDING SYSTEM (IBS)


It is a system which suits all architectural demands & not a machine or component



Model Installation

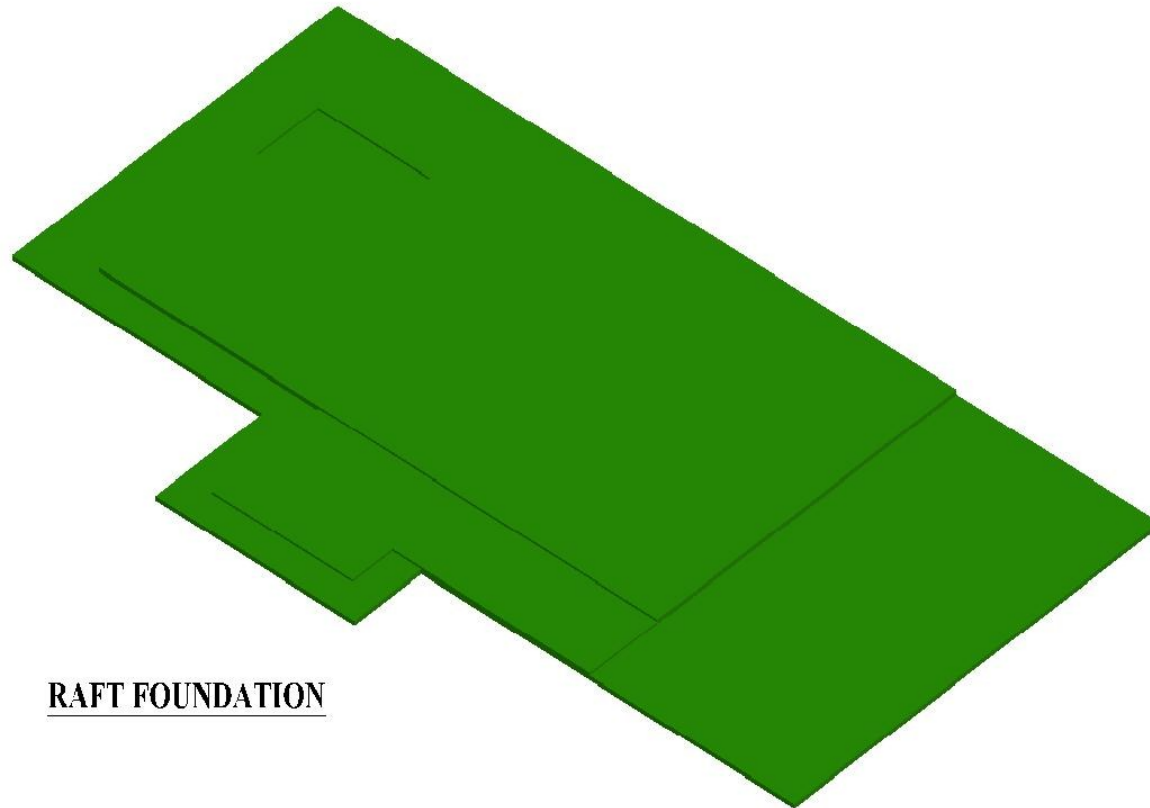

RAFT FOUNDATION

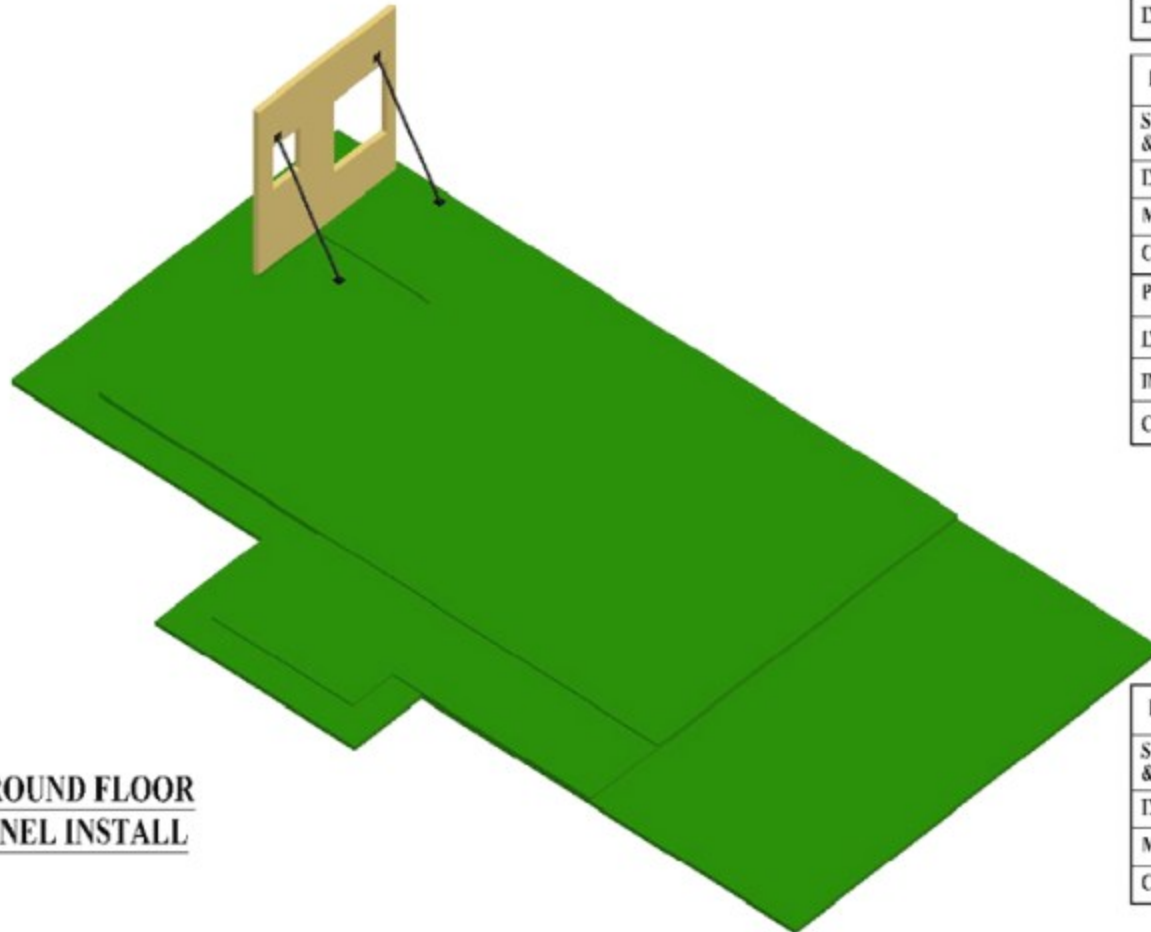


GROUND FLOOR
PANEL INSTALL

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

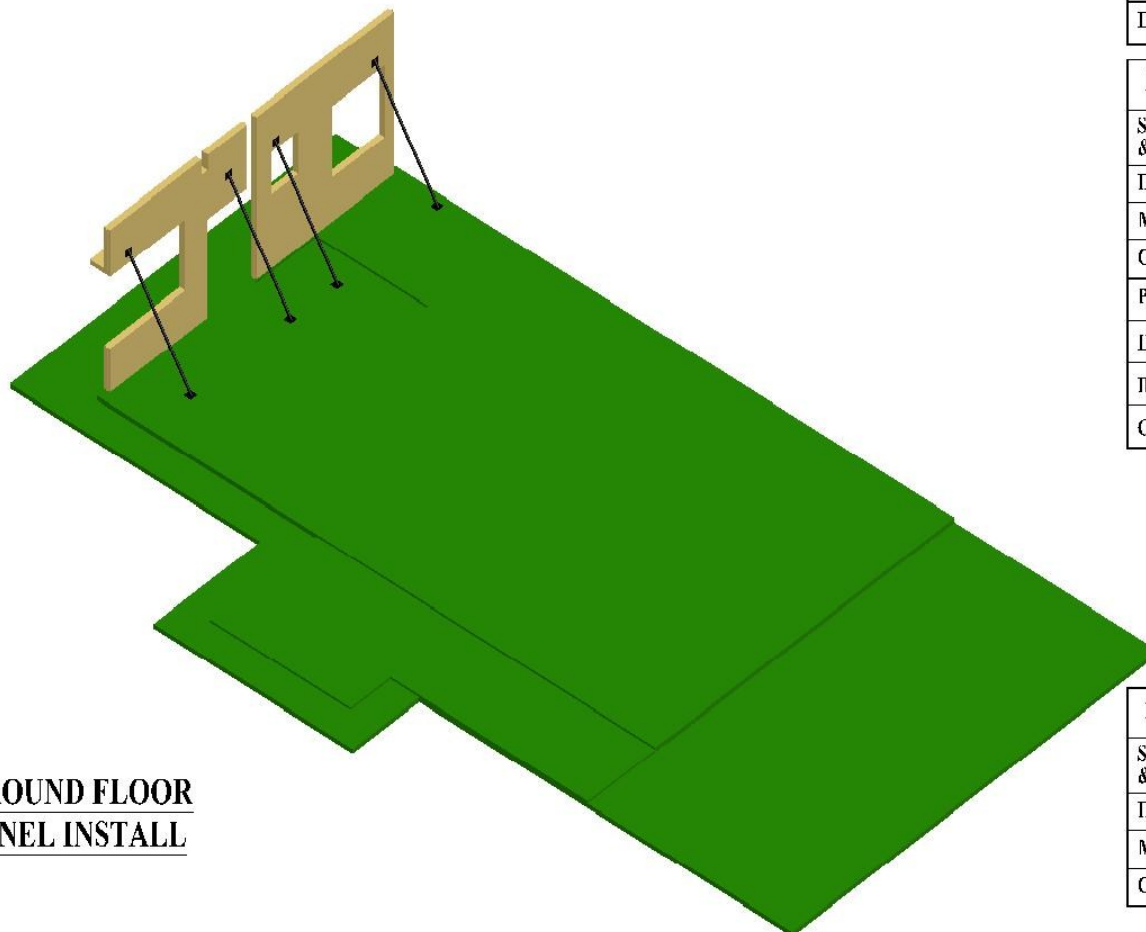


GROUND FLOOR
PANEL INSTALL

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

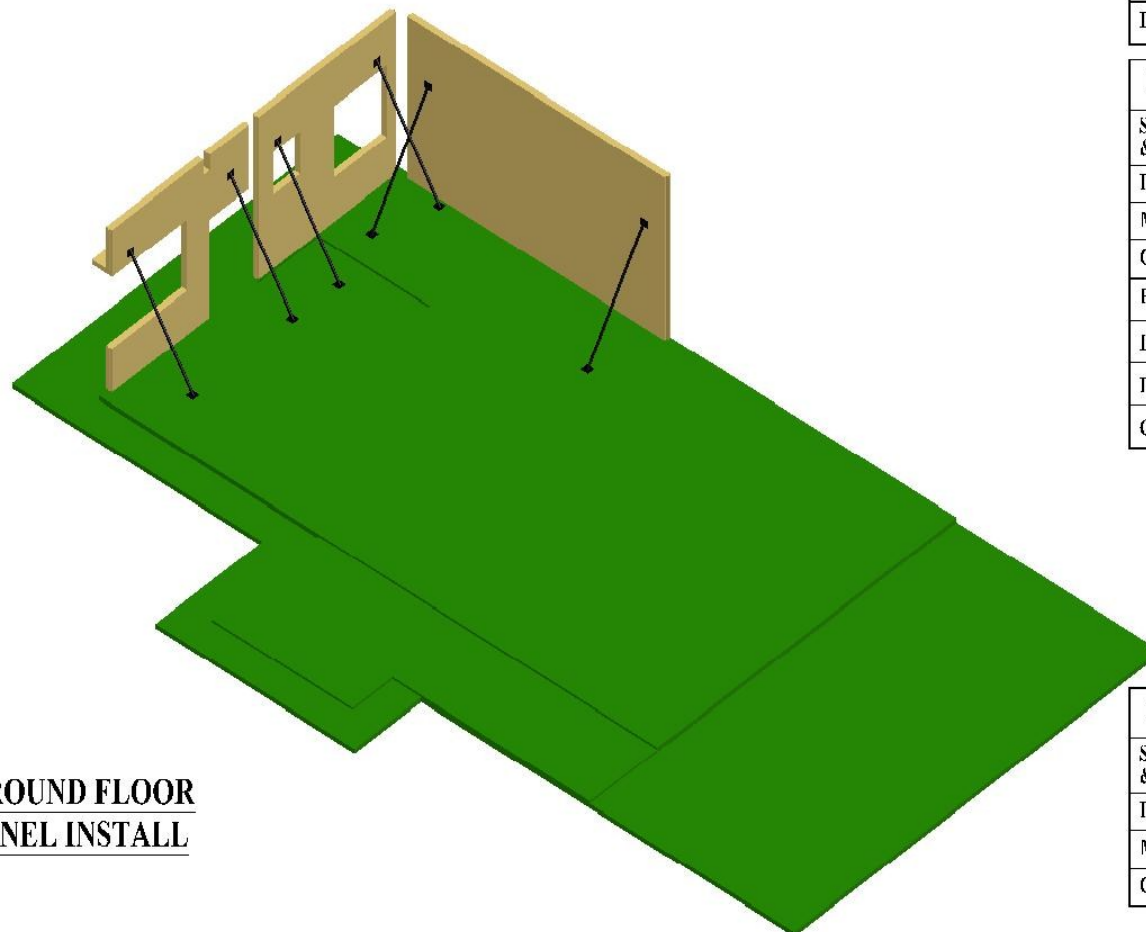


GROUND FLOOR
PANEL INSTALL

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

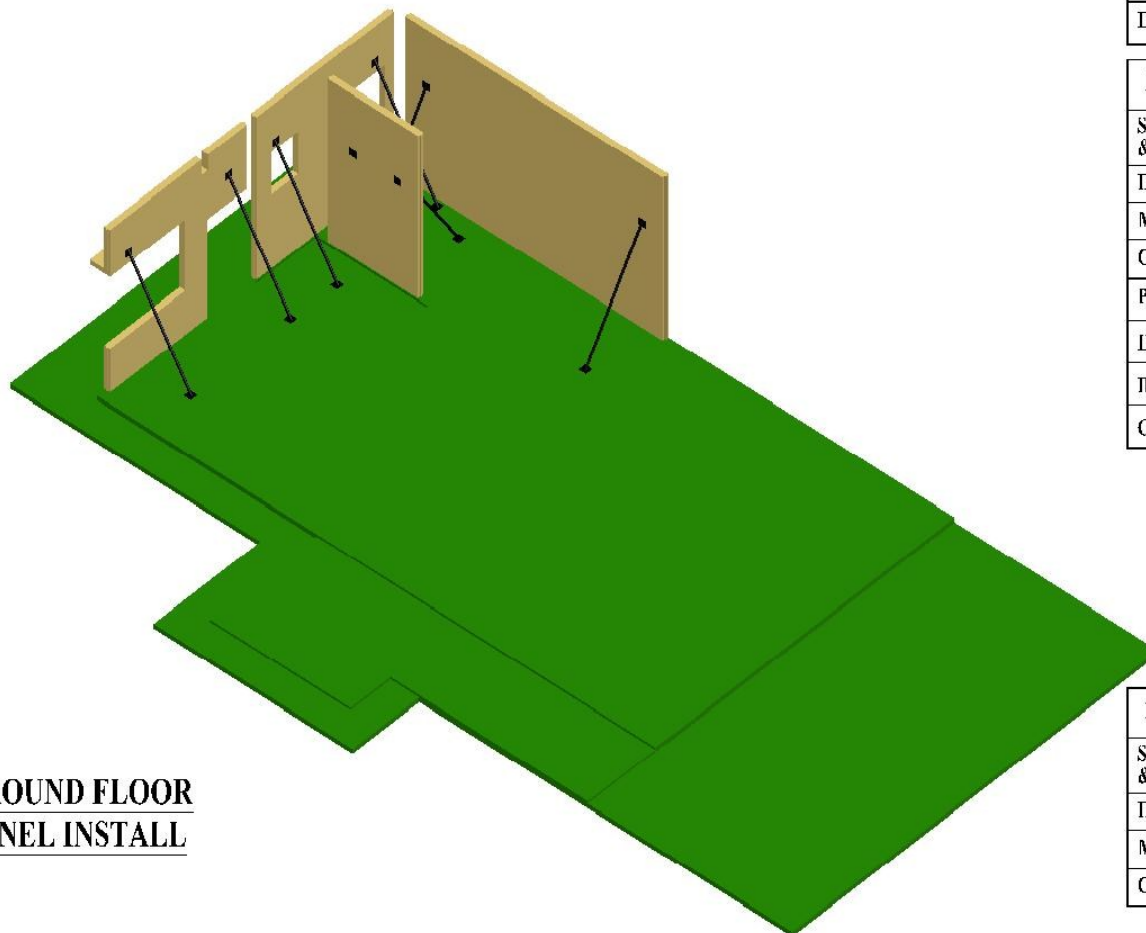


GROUND FLOOR
PANEL INSTALL

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

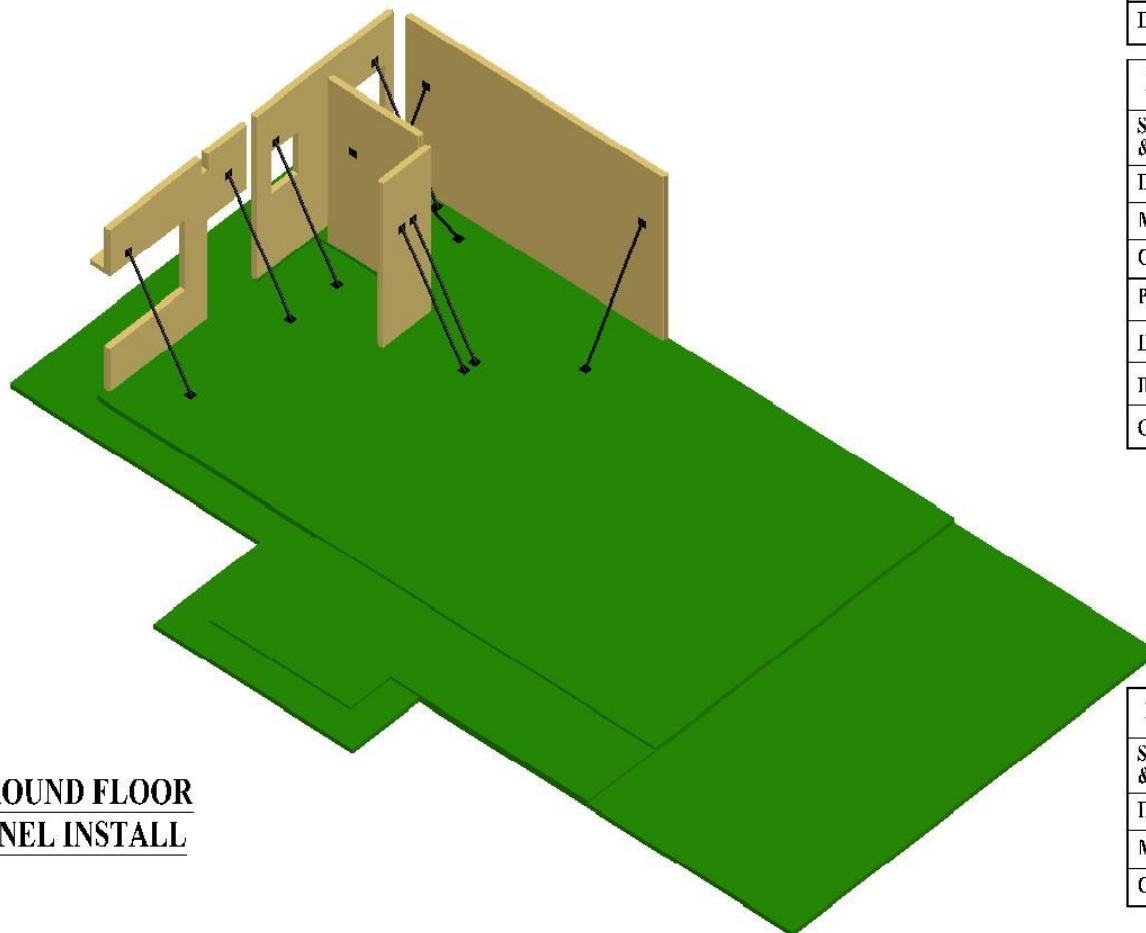


GROUND FLOOR
PANEL INSTALL

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

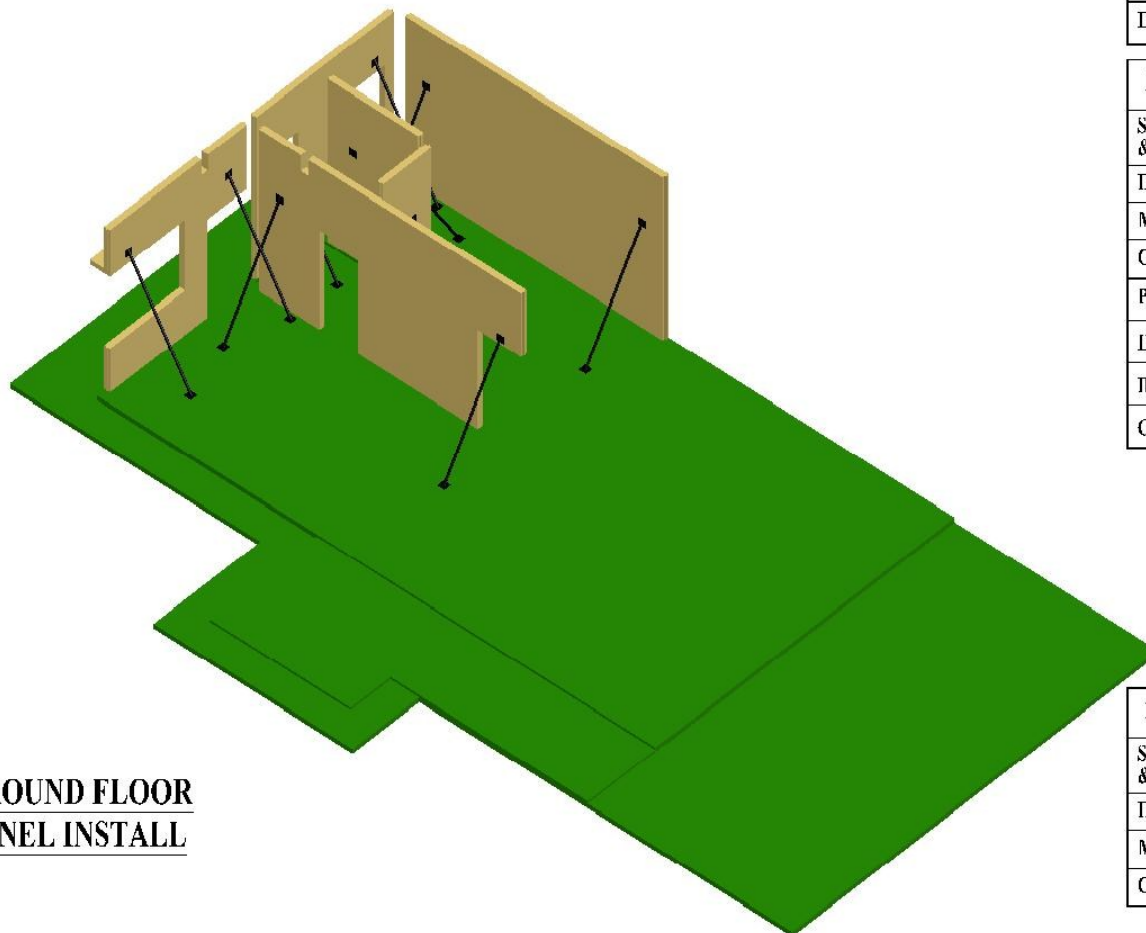


GROUND FLOOR
PANEL INSTALL

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit

INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

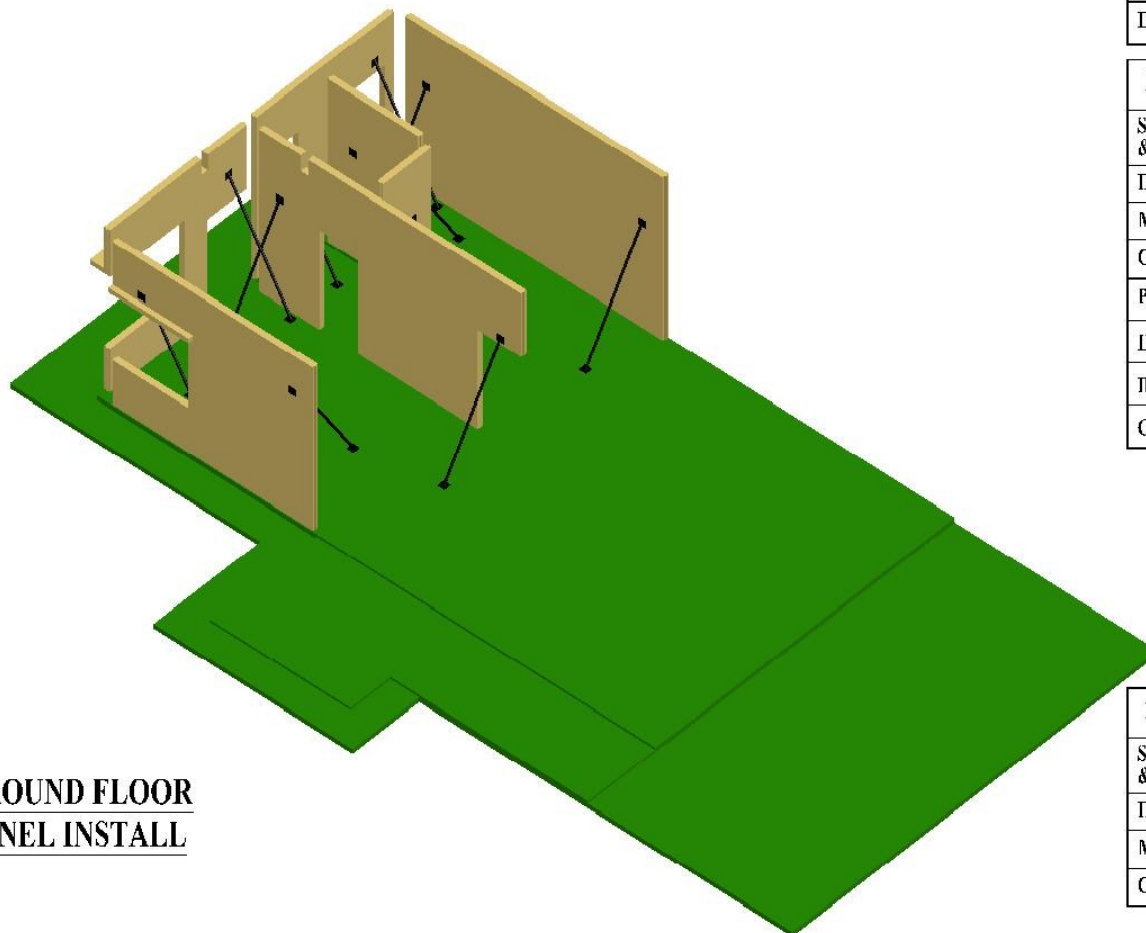


GROUND FLOOR
PANEL INSTALL

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

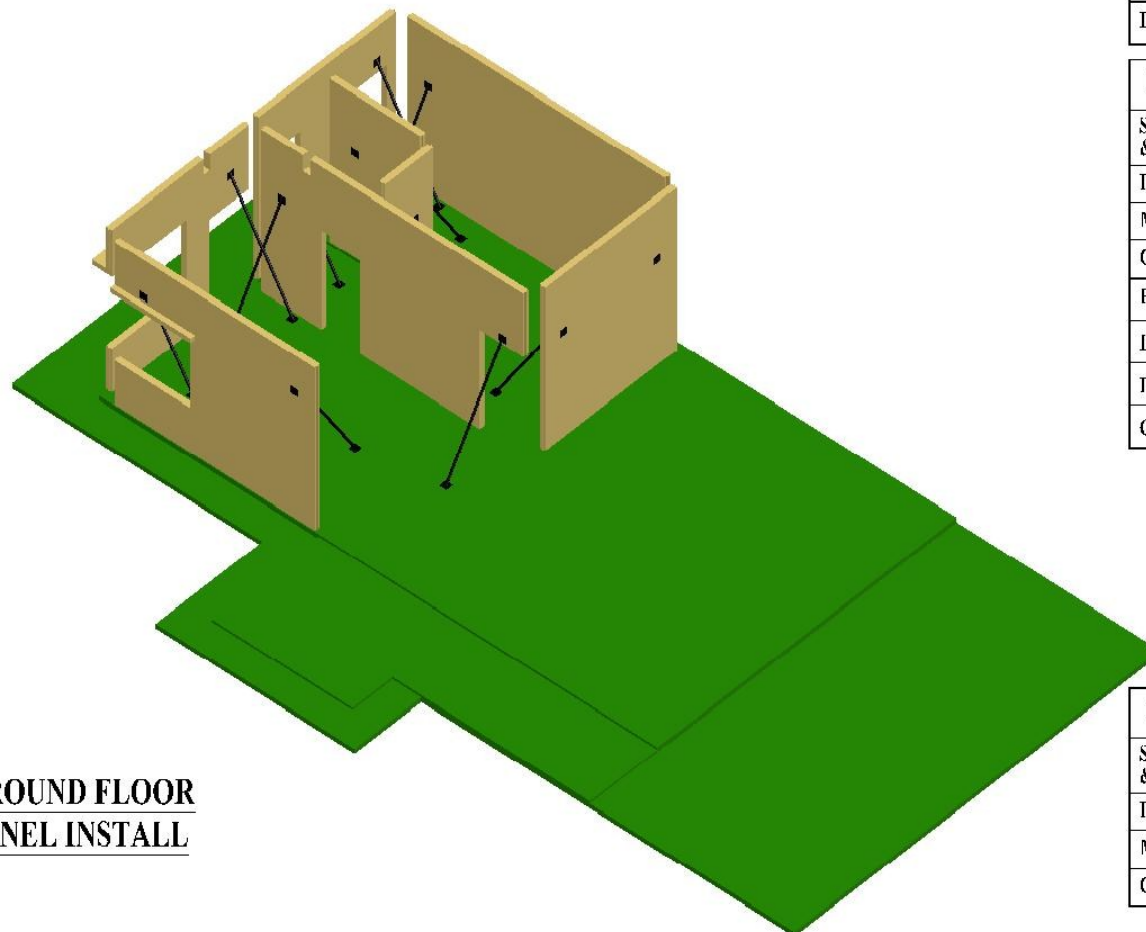


GROUND FLOOR
PANEL INSTALL

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

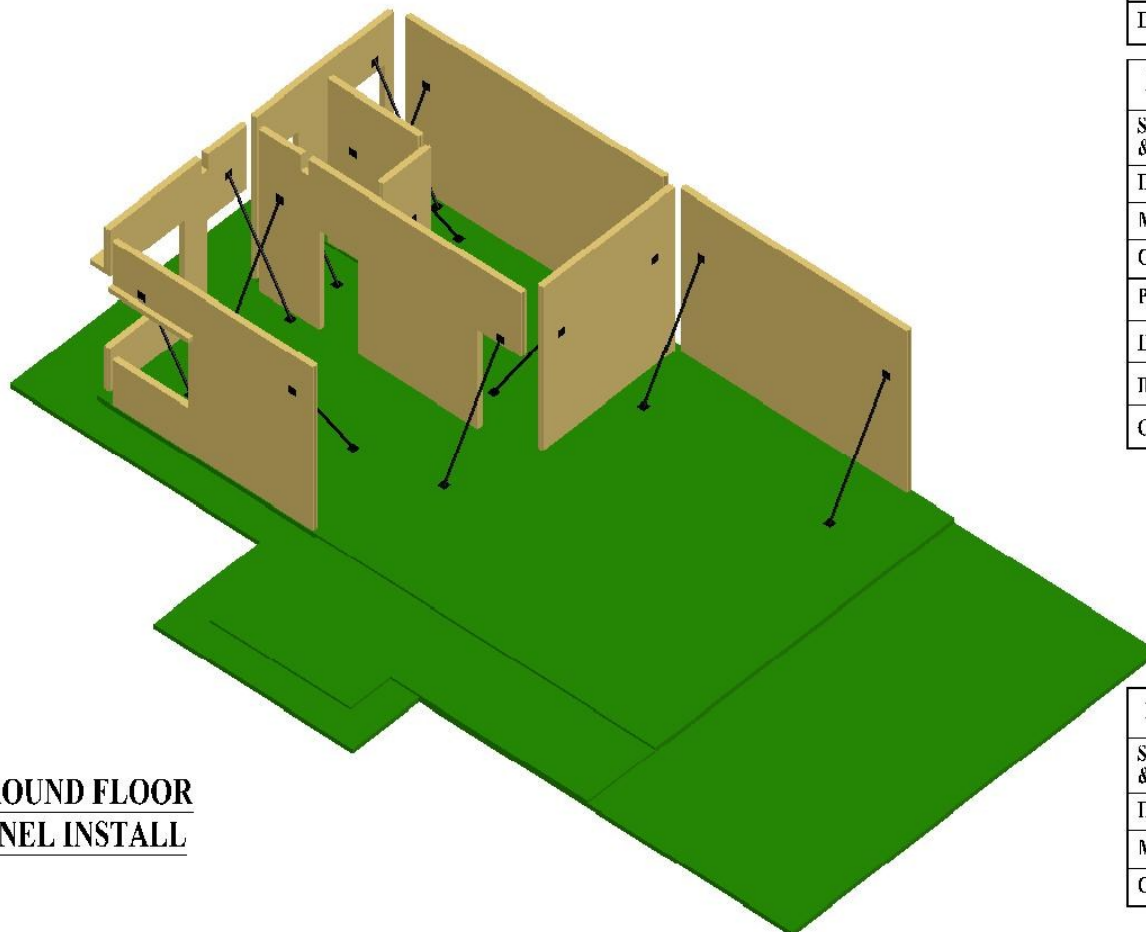


GROUND FLOOR
PANEL INSTALL

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

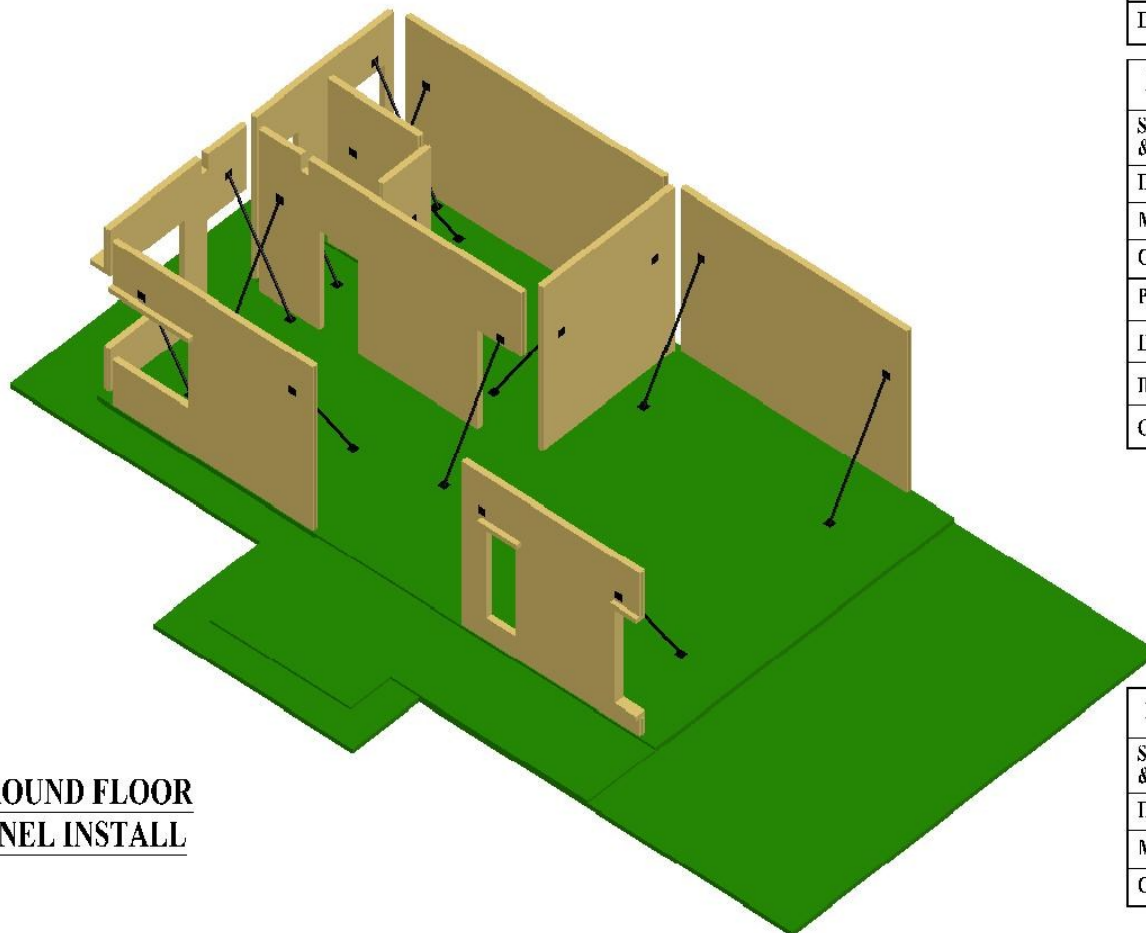


GROUND FLOOR
PANEL INSTALL

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

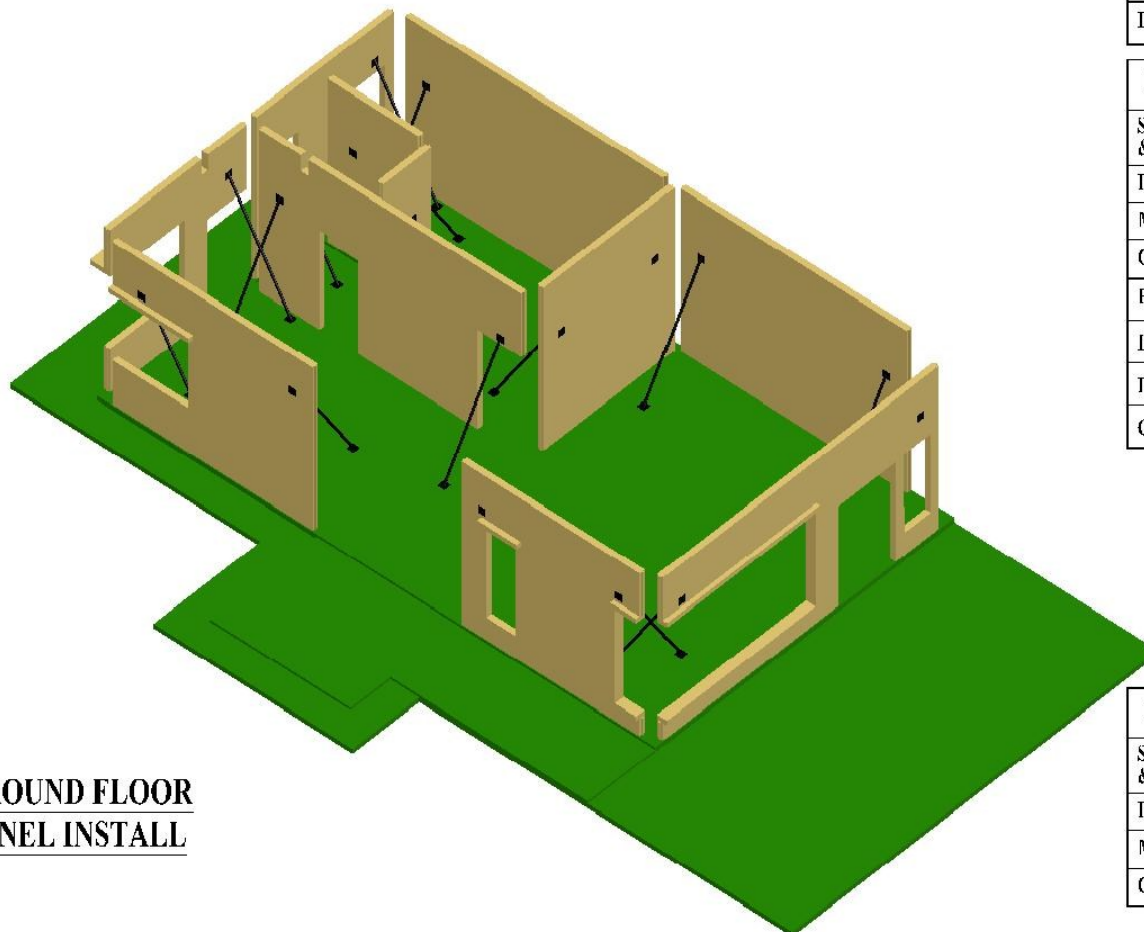


GROUND FLOOR
PANEL INSTALL

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

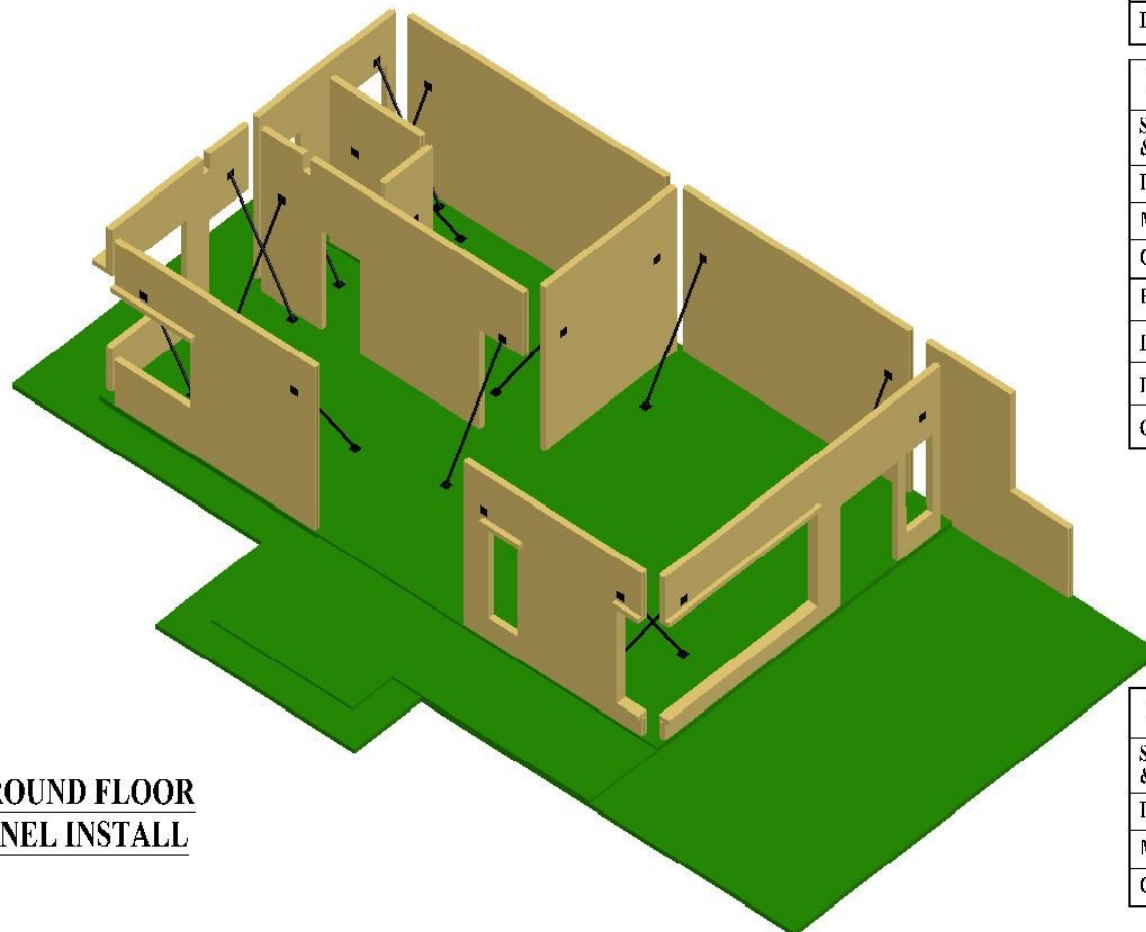


GROUND FLOOR
PANEL INSTALL

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

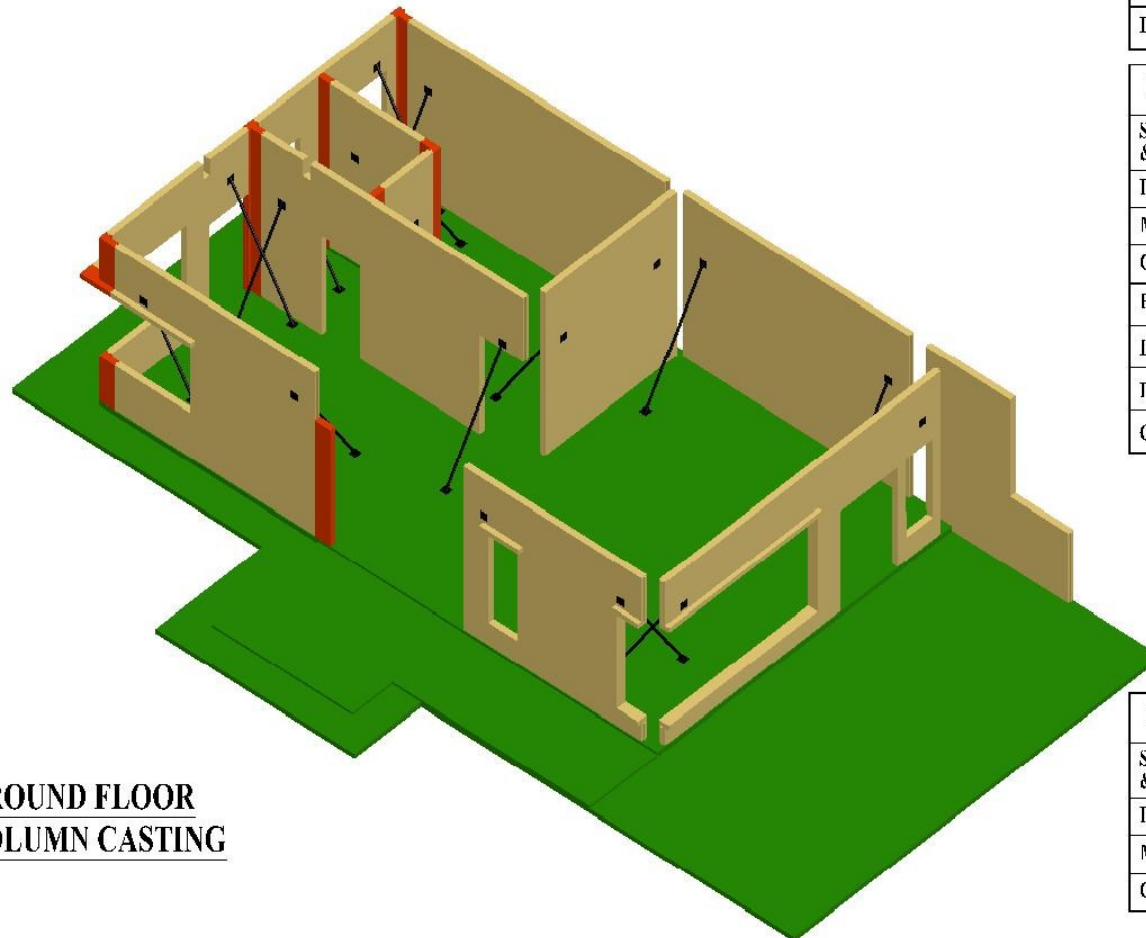


**GROUND FLOOR
COLUMN CASTING**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

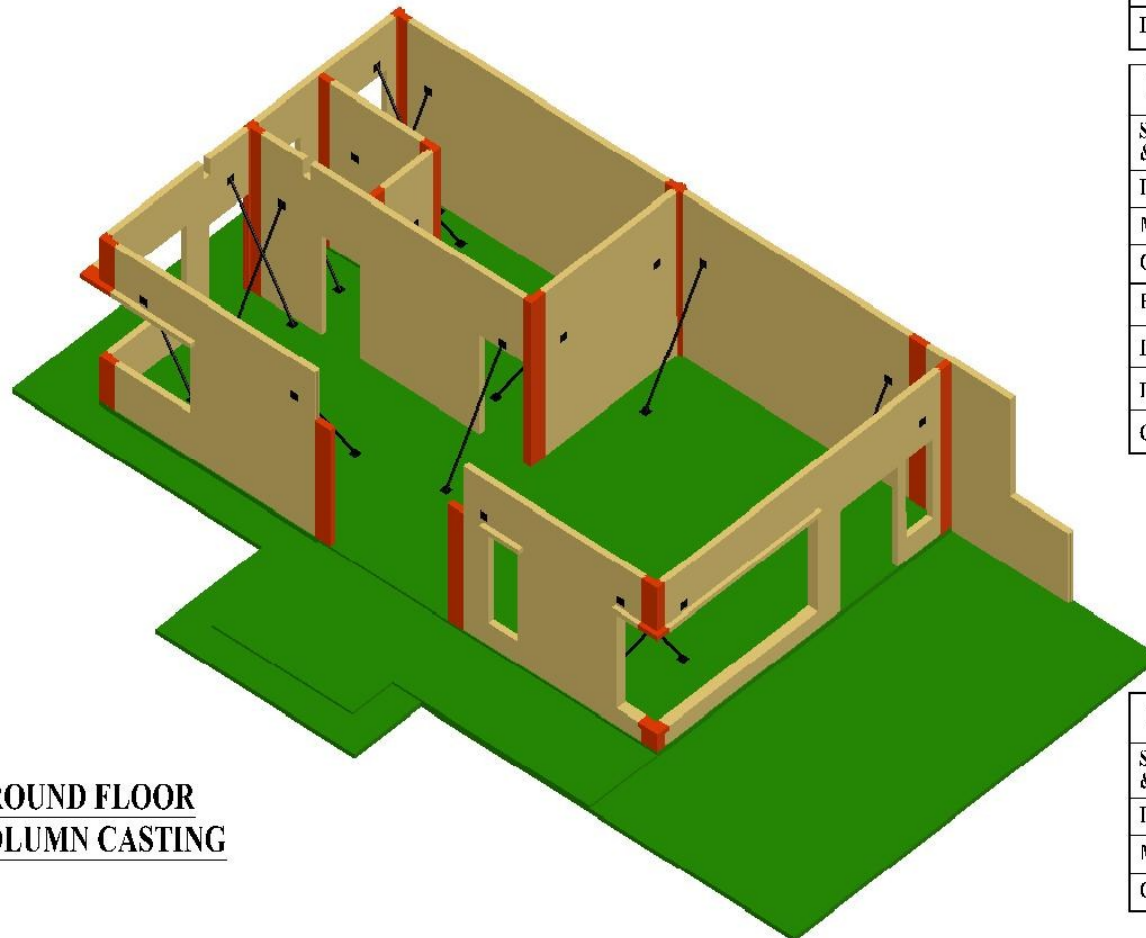


**GROUND FLOOR
COLUMN CASTING**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

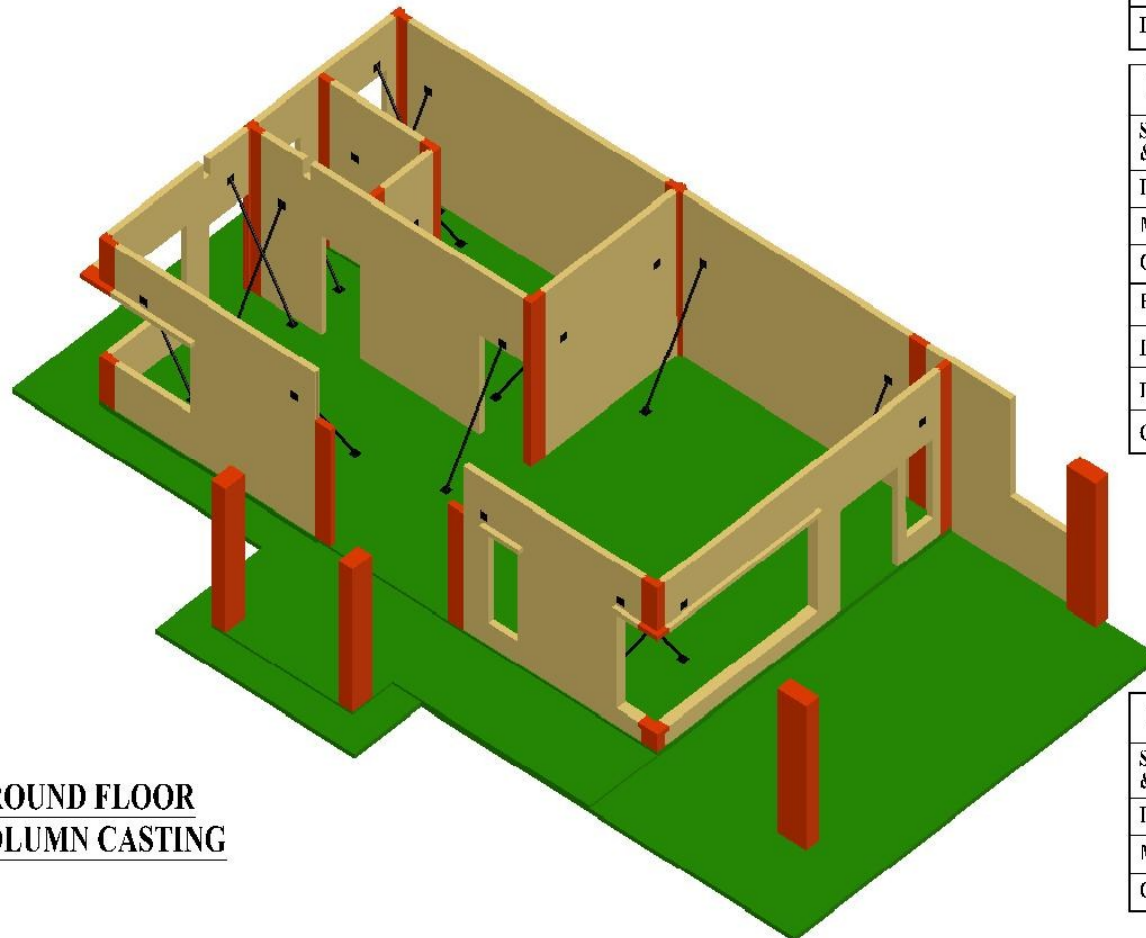


**GROUND FLOOR
COLUMN CASTING**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

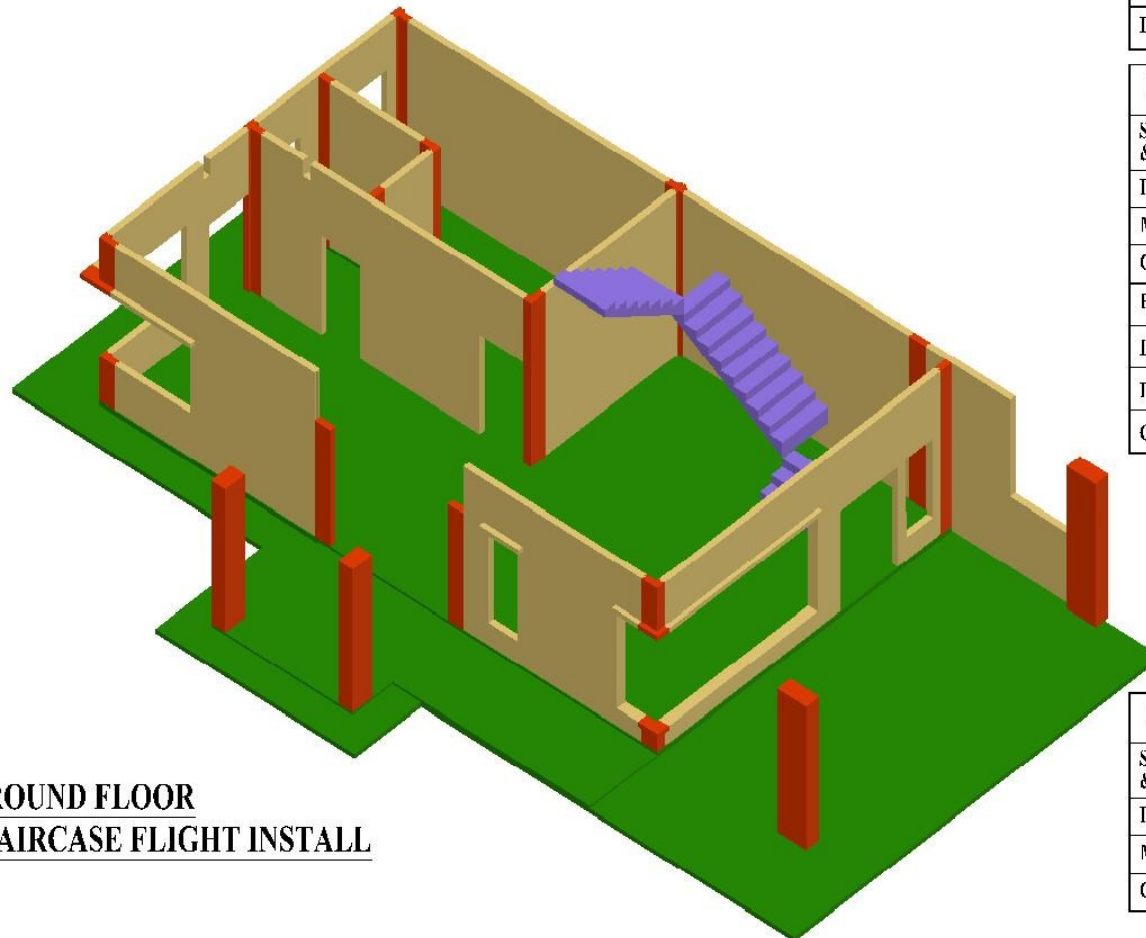


**GROUND FLOOR
STAIRCASE FLIGHT INSTALL**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

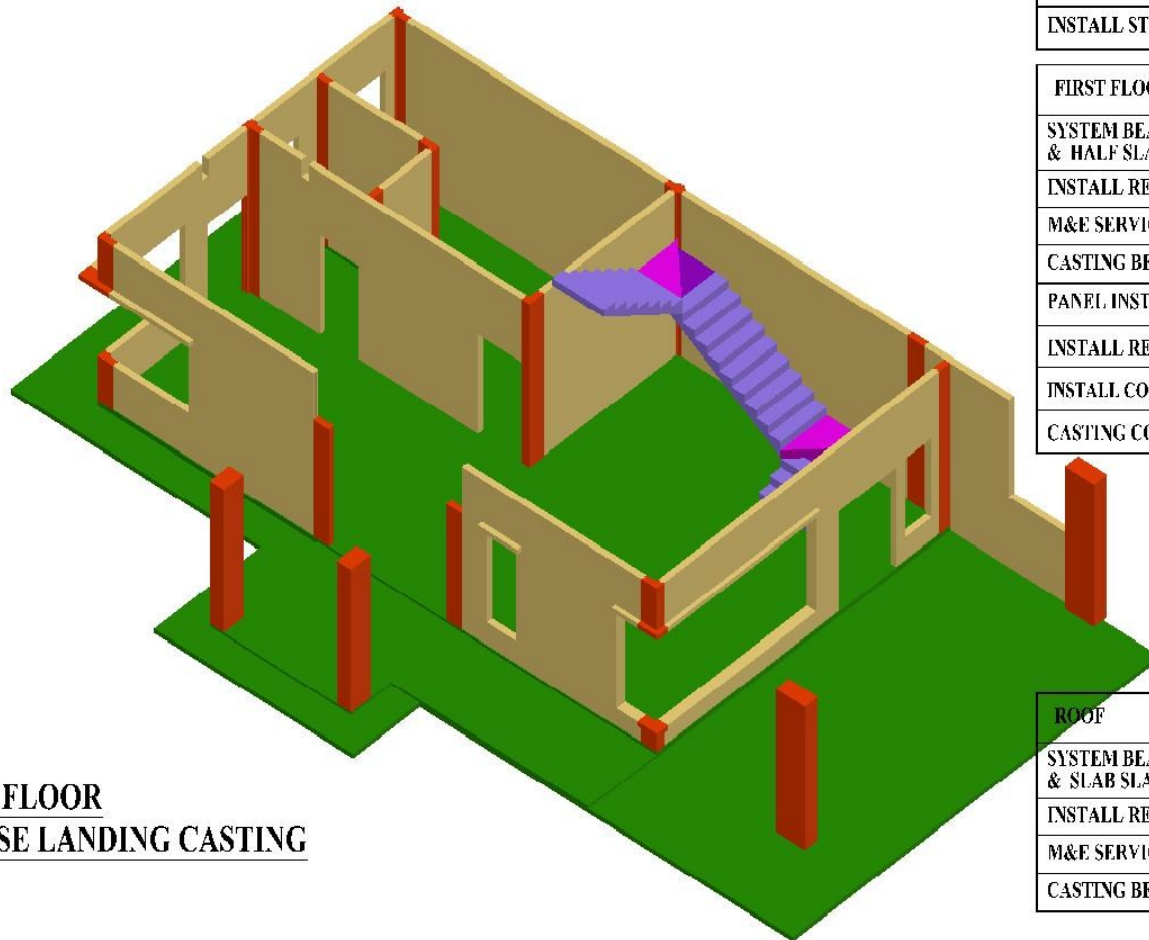


**GROUND FLOOR
STAIRCASE LANDING CASTING**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

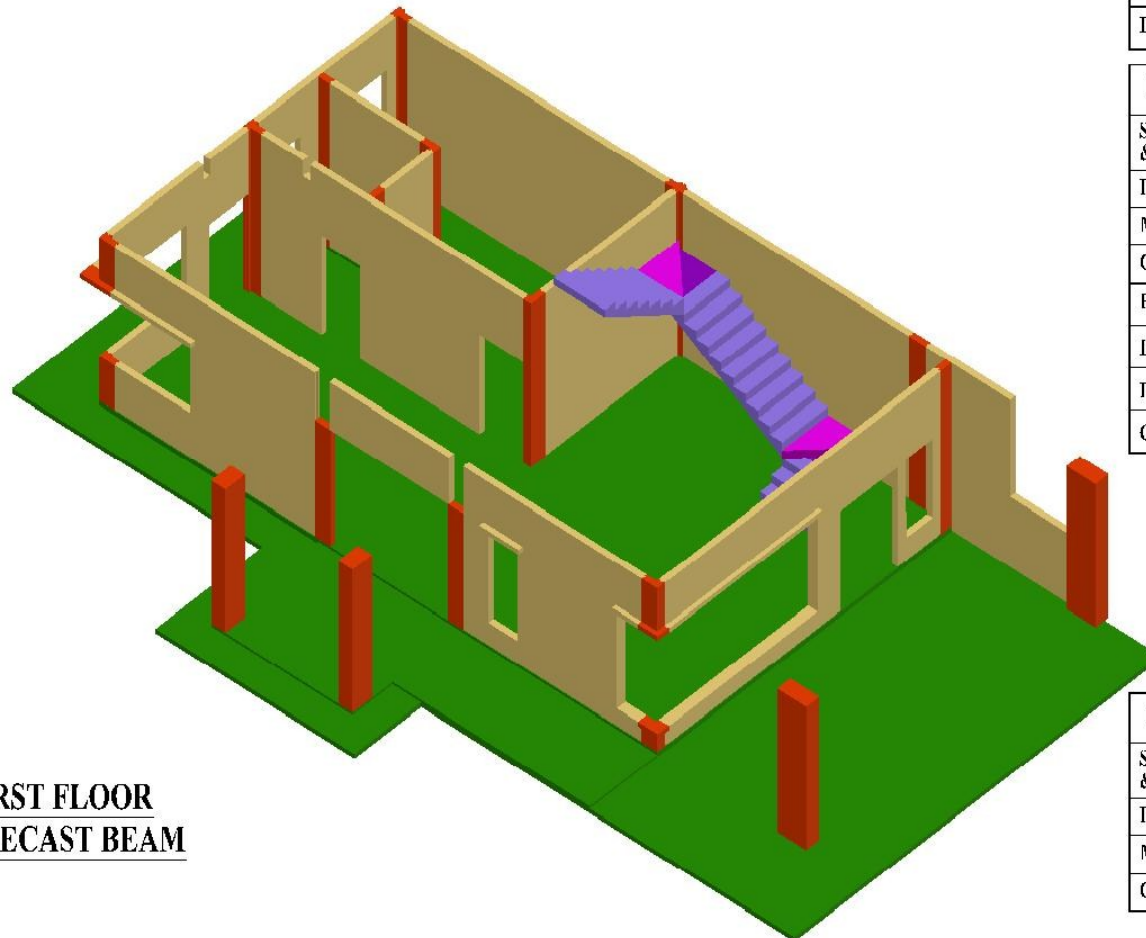


**FIRST FLOOR
PRECAST BEAM**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

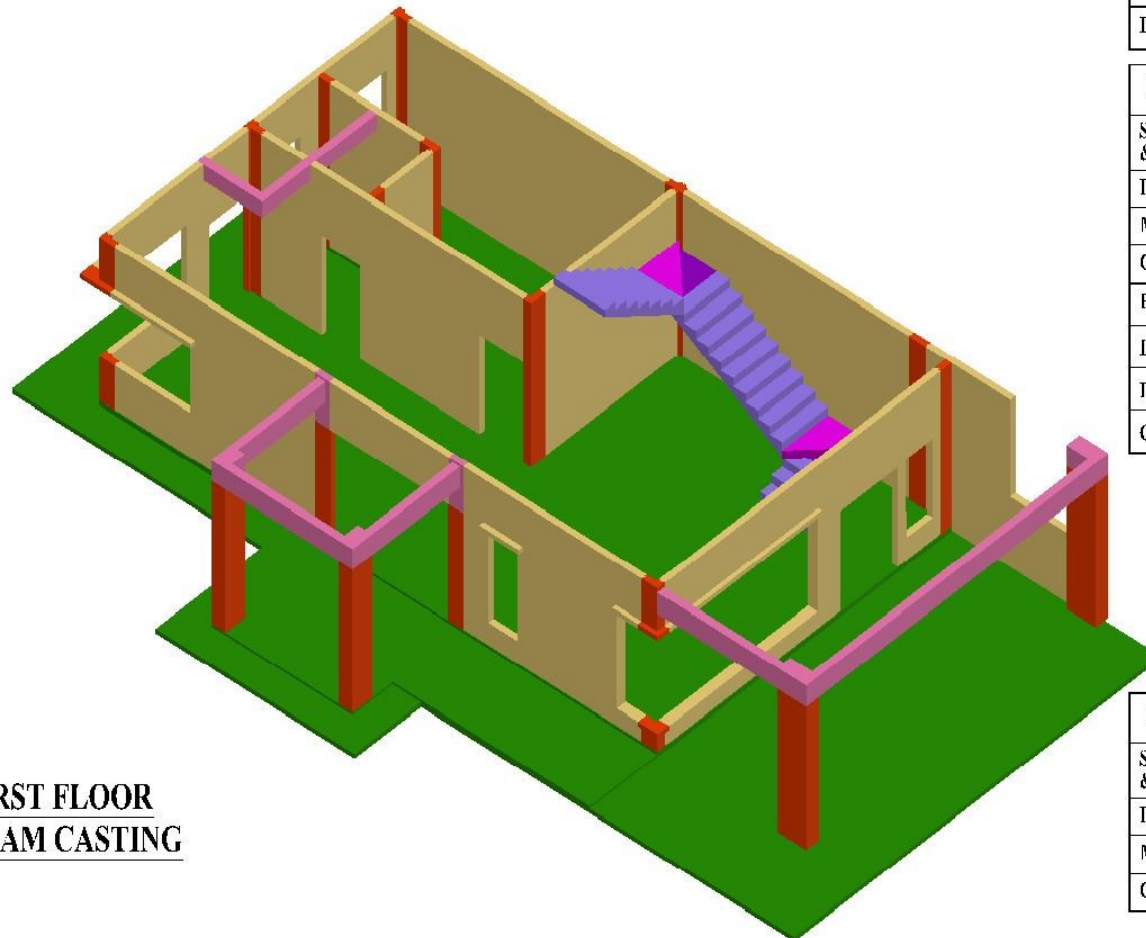


**FIRST FLOOR
BEAM CASTING**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

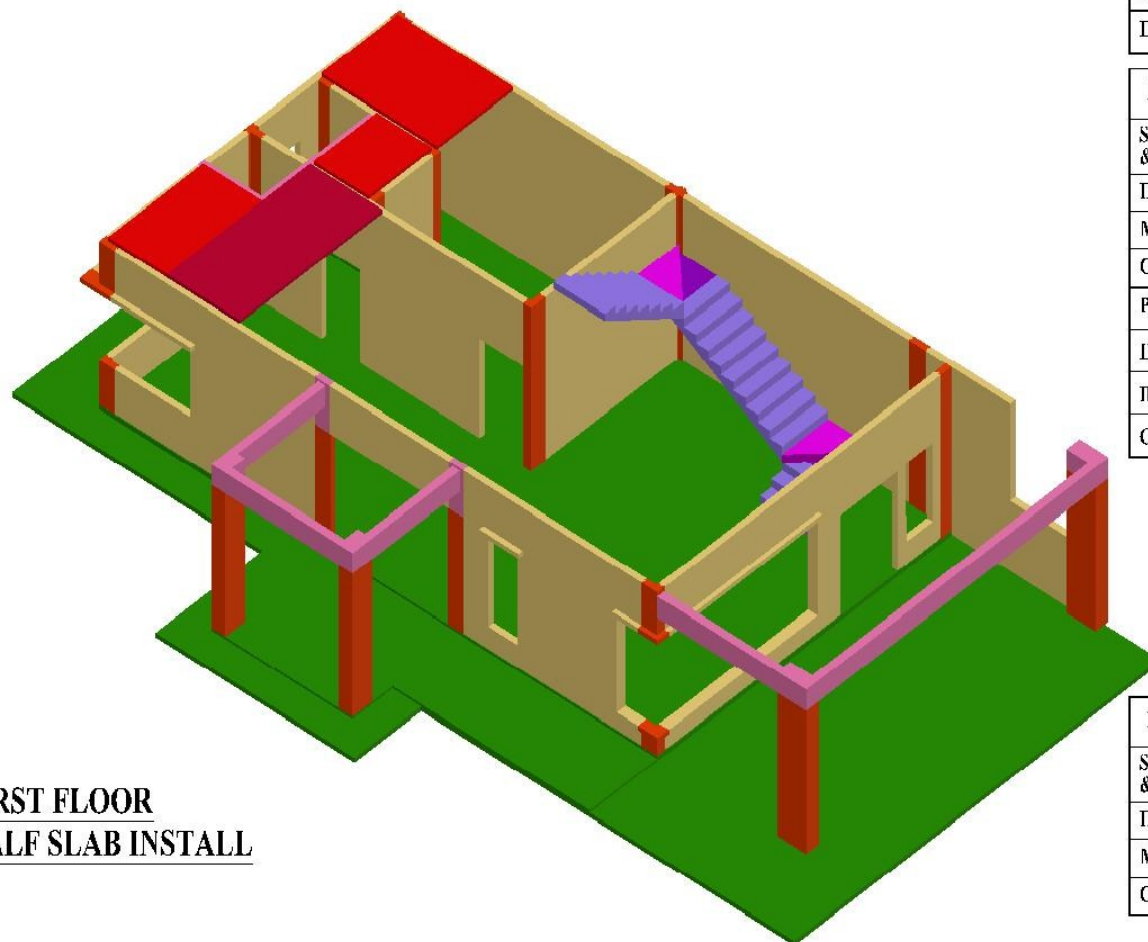


**FIRST FLOOR
HALF SLAB INSTALL**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

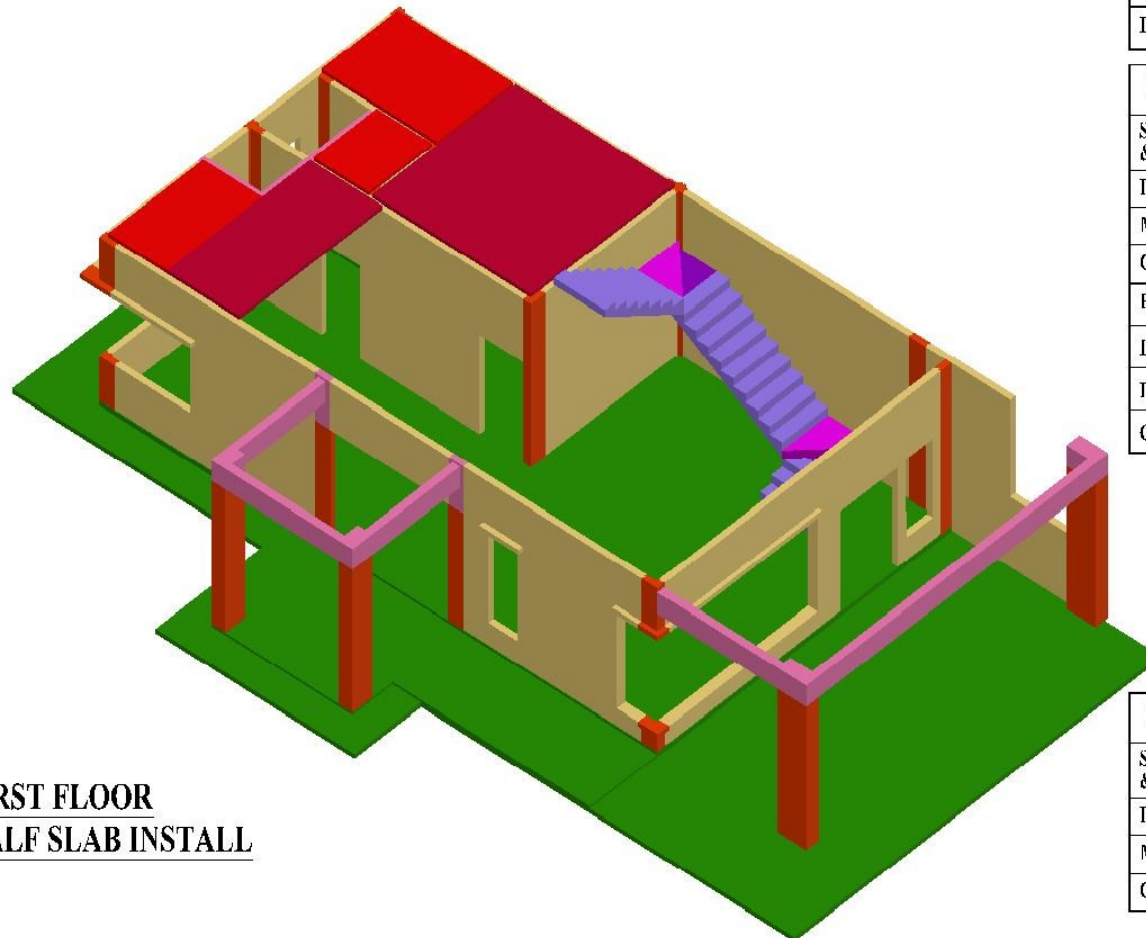


**FIRST FLOOR
HALF SLAB INSTALL**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

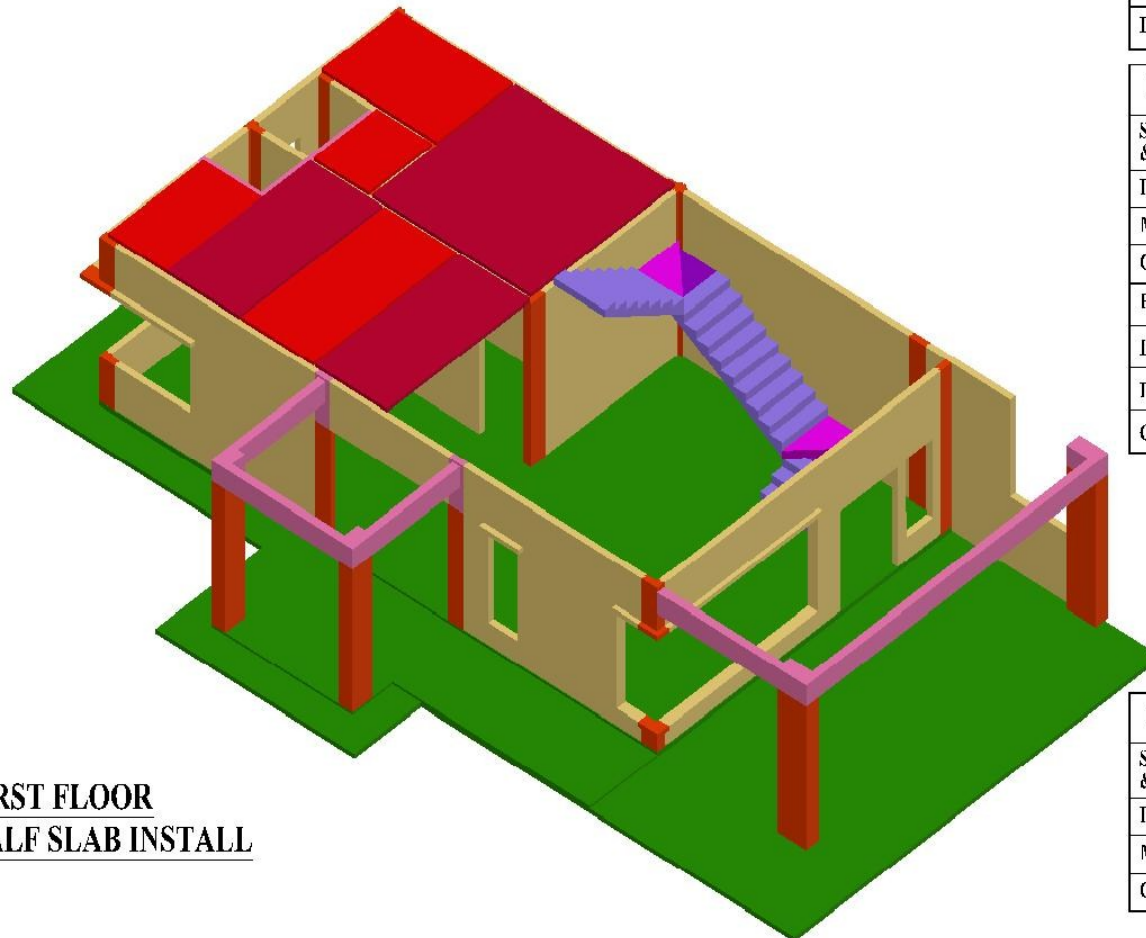


**FIRST FLOOR
HALF SLAB INSTALL**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

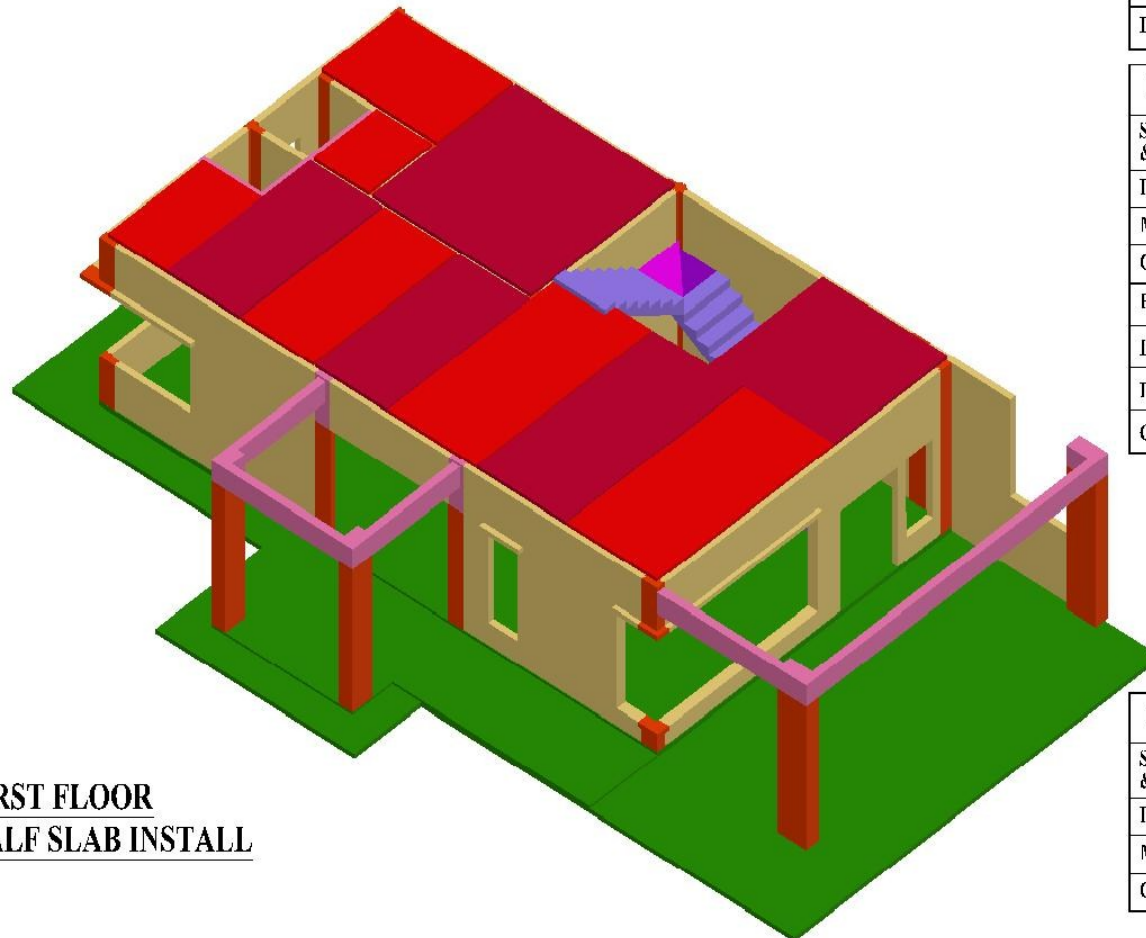


**FIRST FLOOR
HALF SLAB INSTALL**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

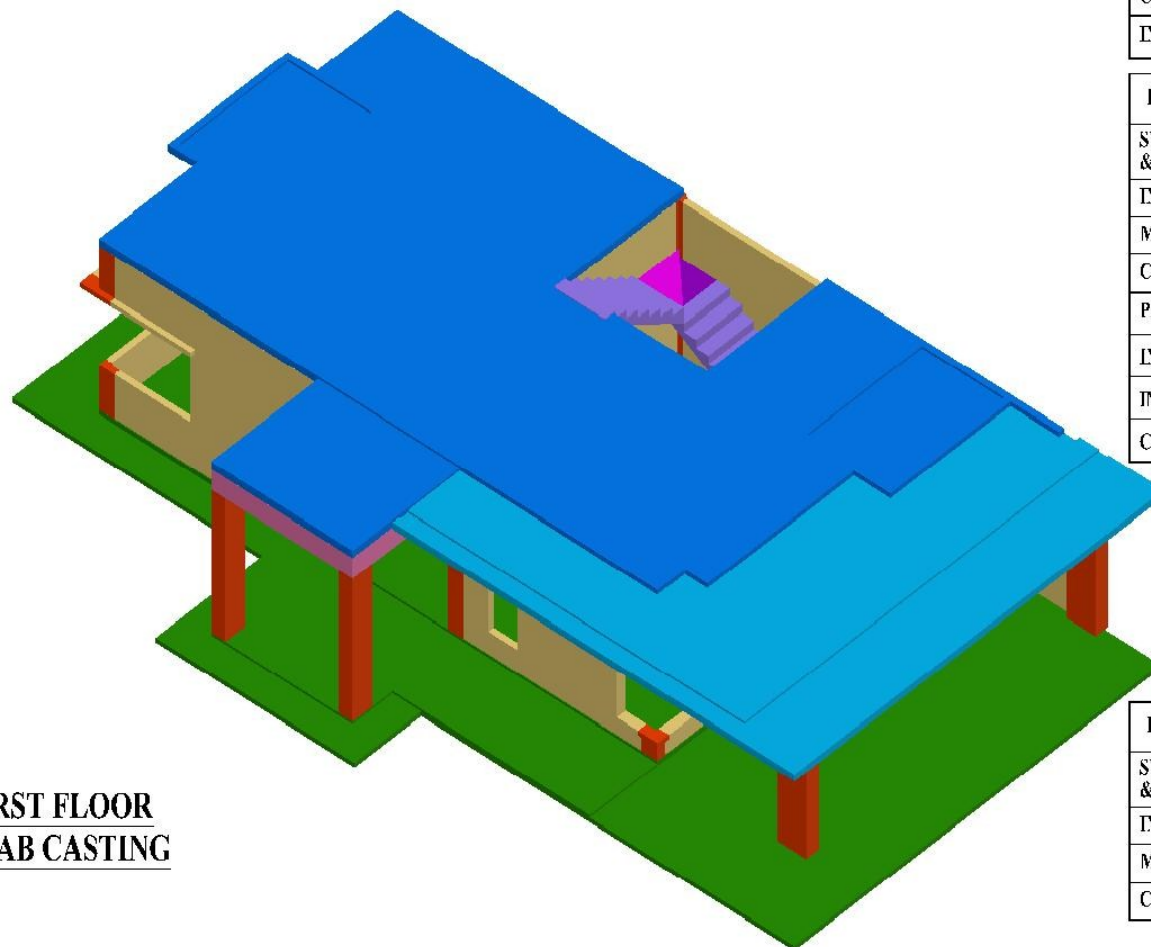


**FIRST FLOOR
SLAB CASTING**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit

INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

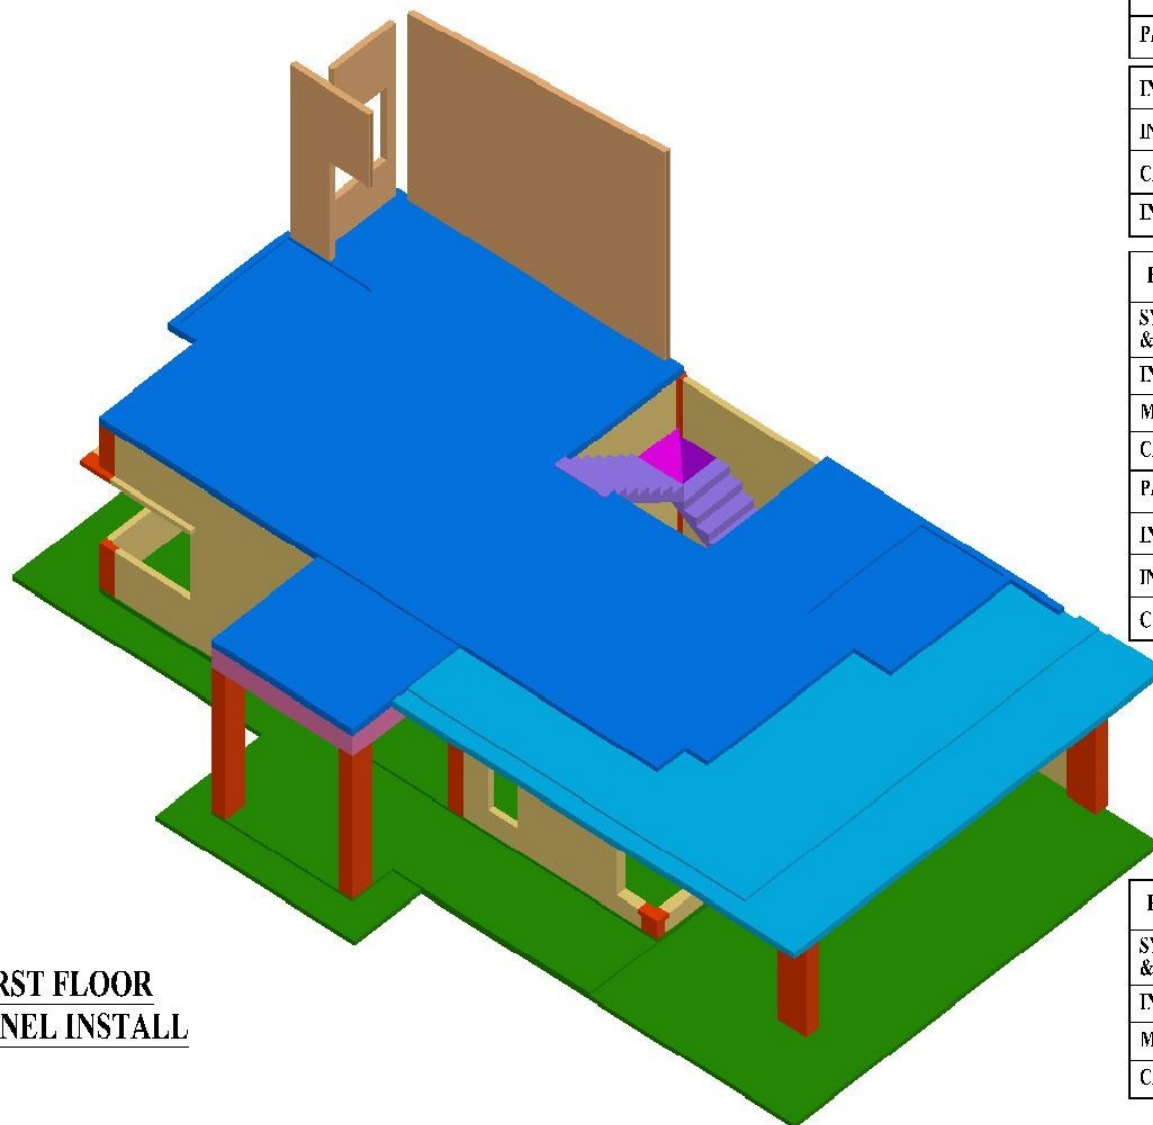


**FIRST FLOOR
PANEL INSTALL**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit

INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

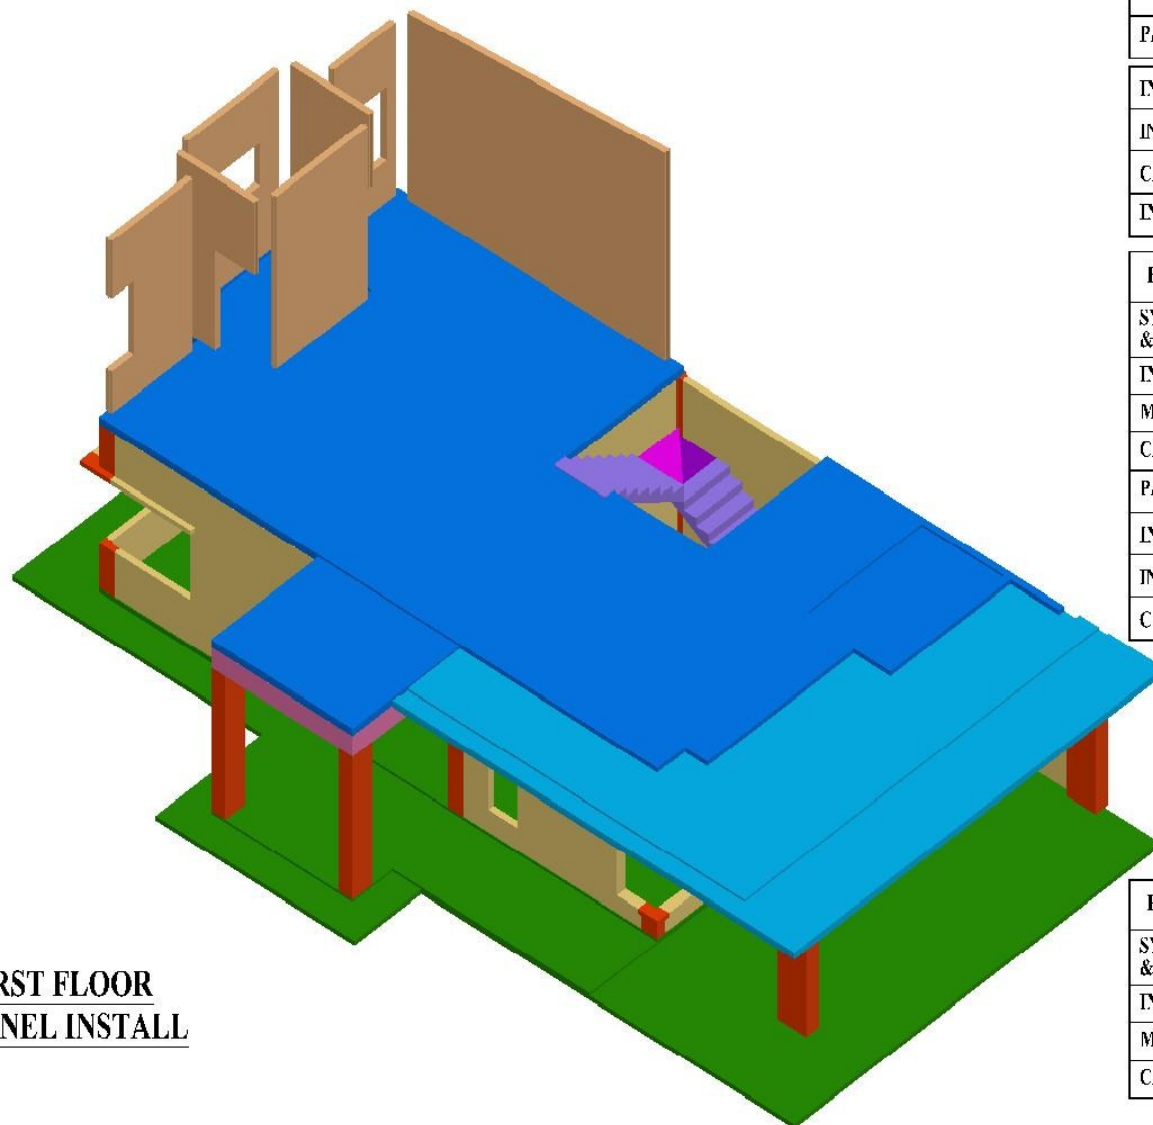


**FIRST FLOOR
PANEL INSTALL**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit

INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

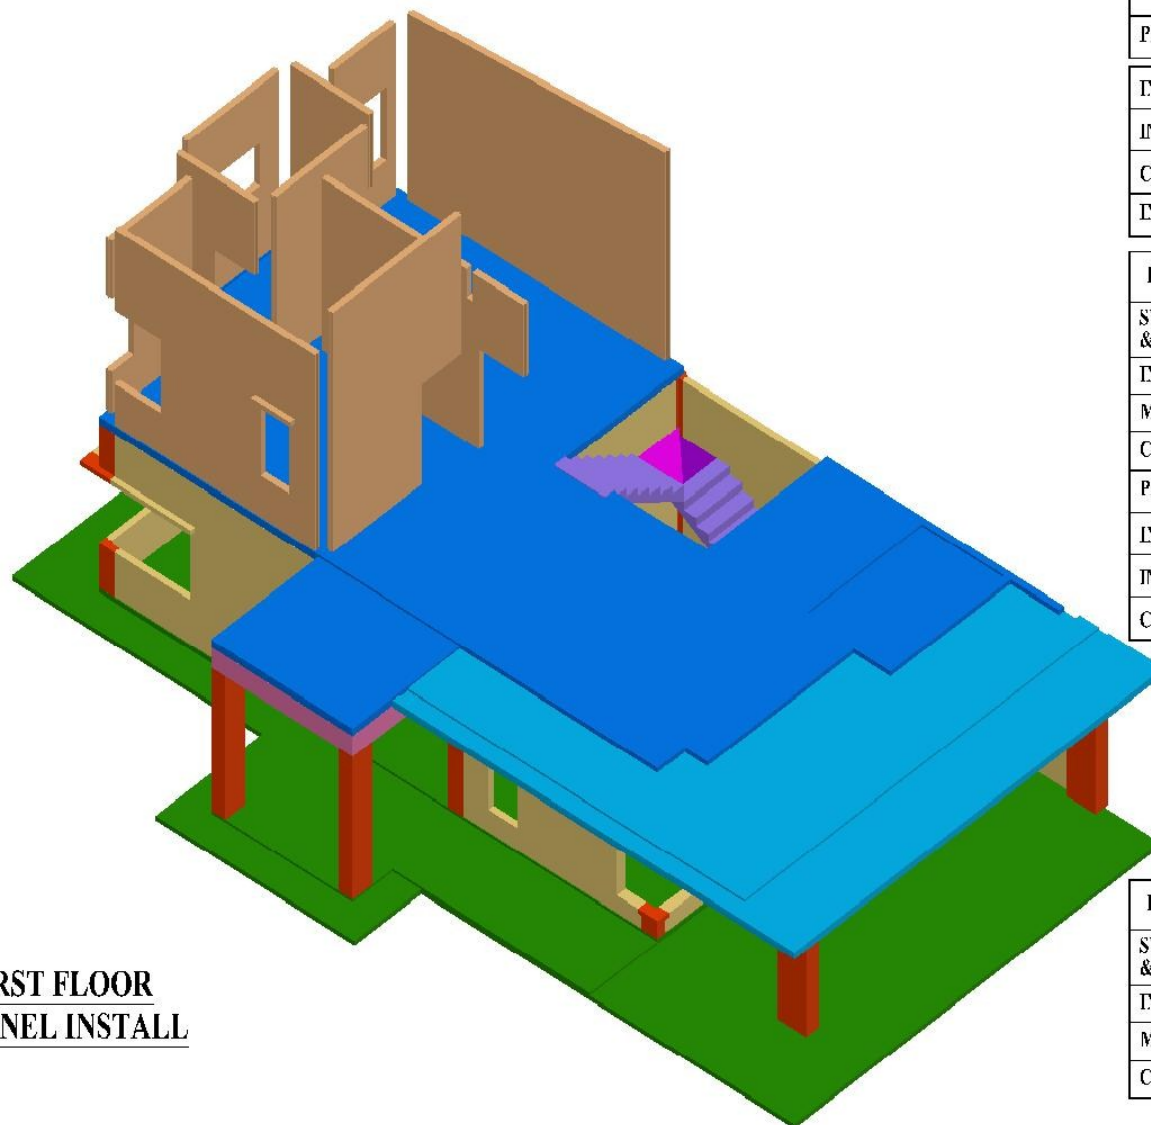


**FIRST FLOOR
PANEL INSTALL**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit

INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

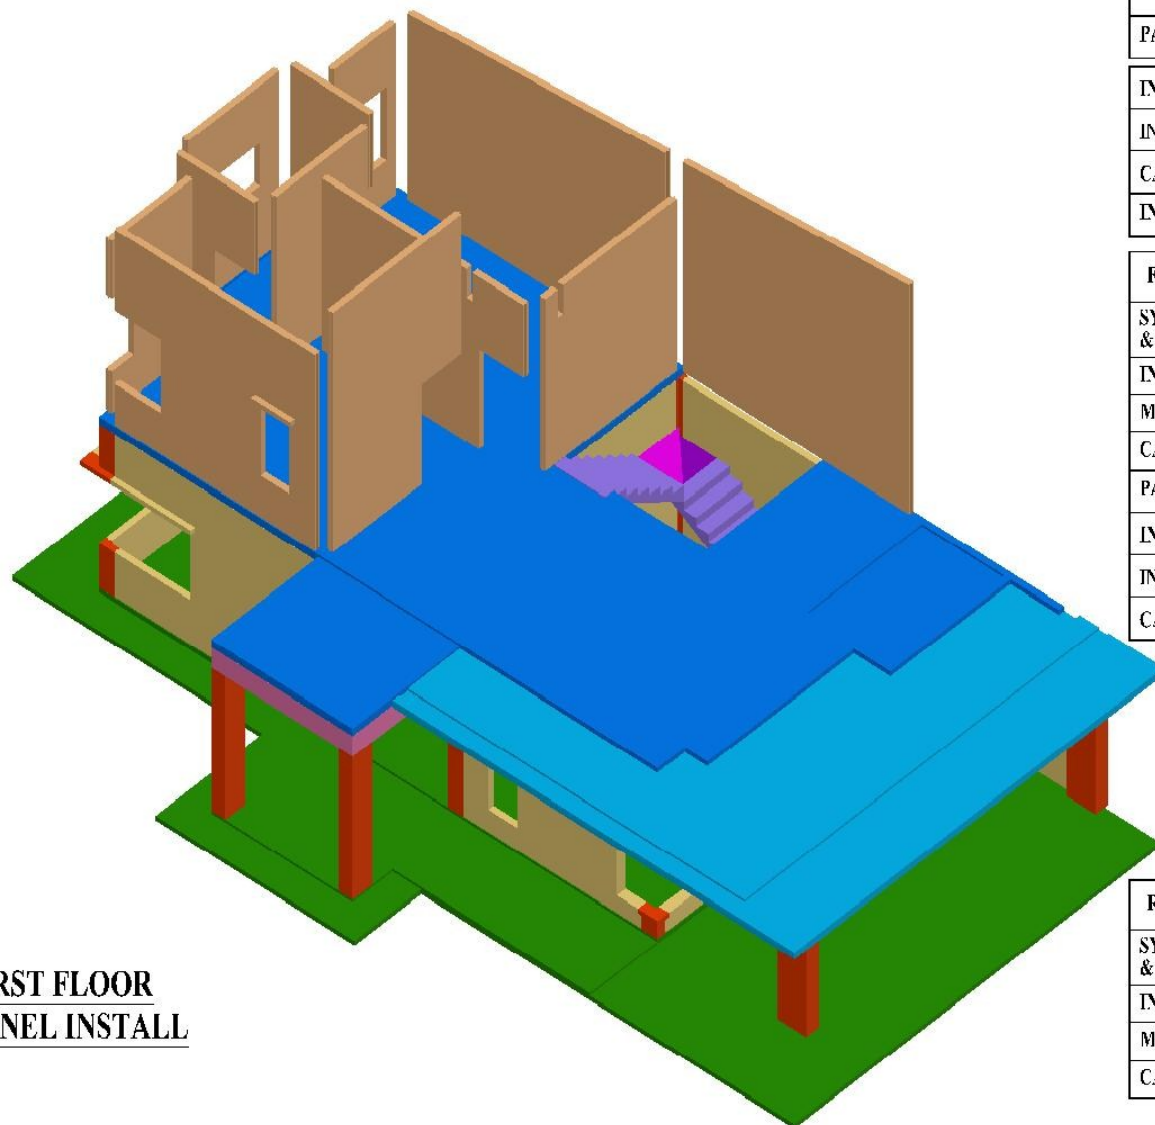


**FIRST FLOOR
PANEL INSTALL**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

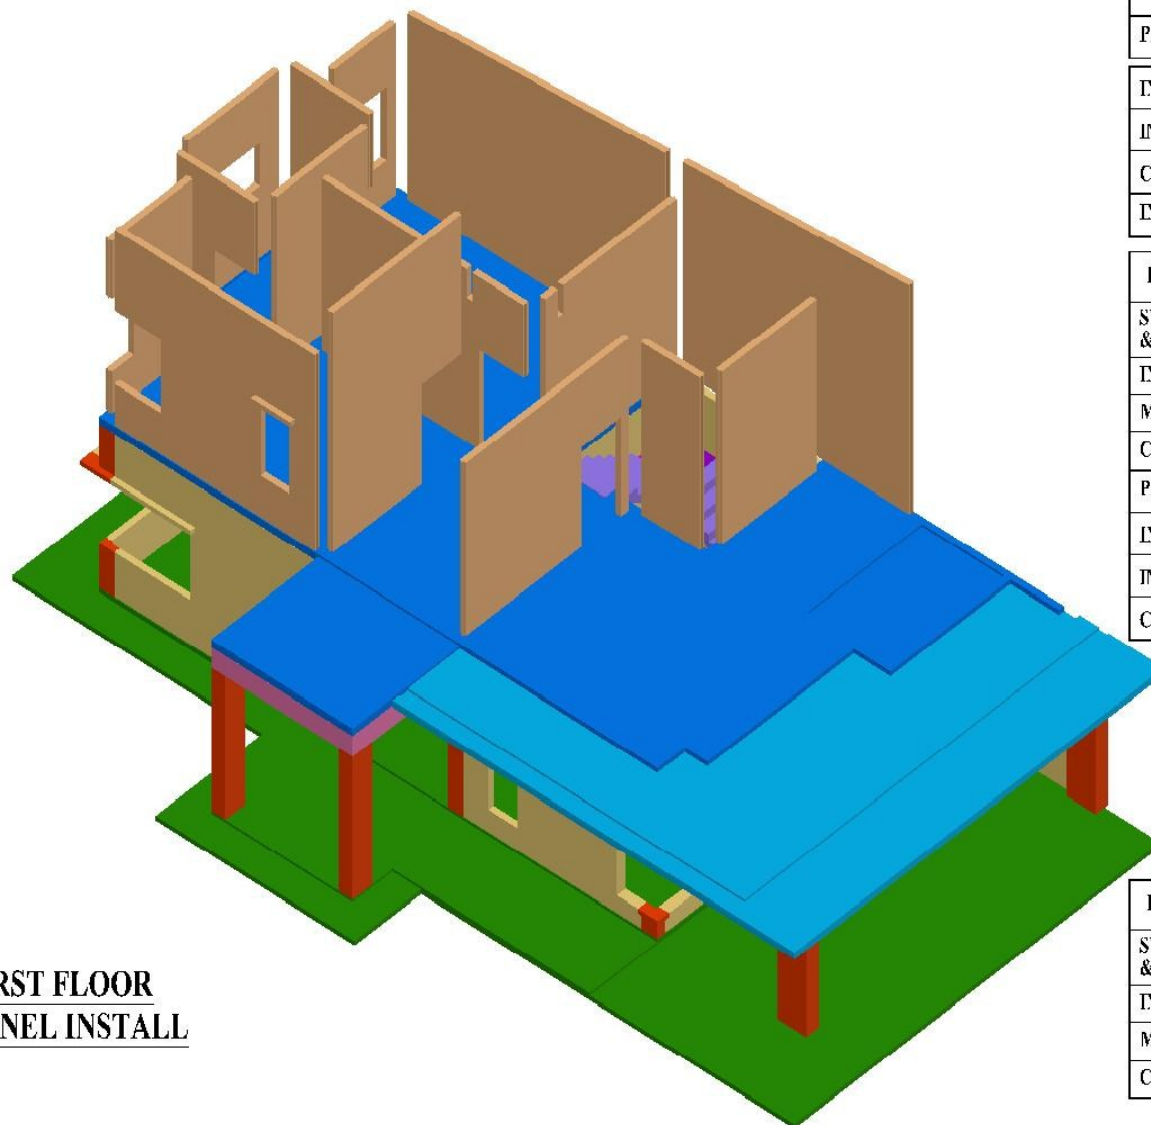


**FIRST FLOOR
PANEL INSTALL**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit

INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

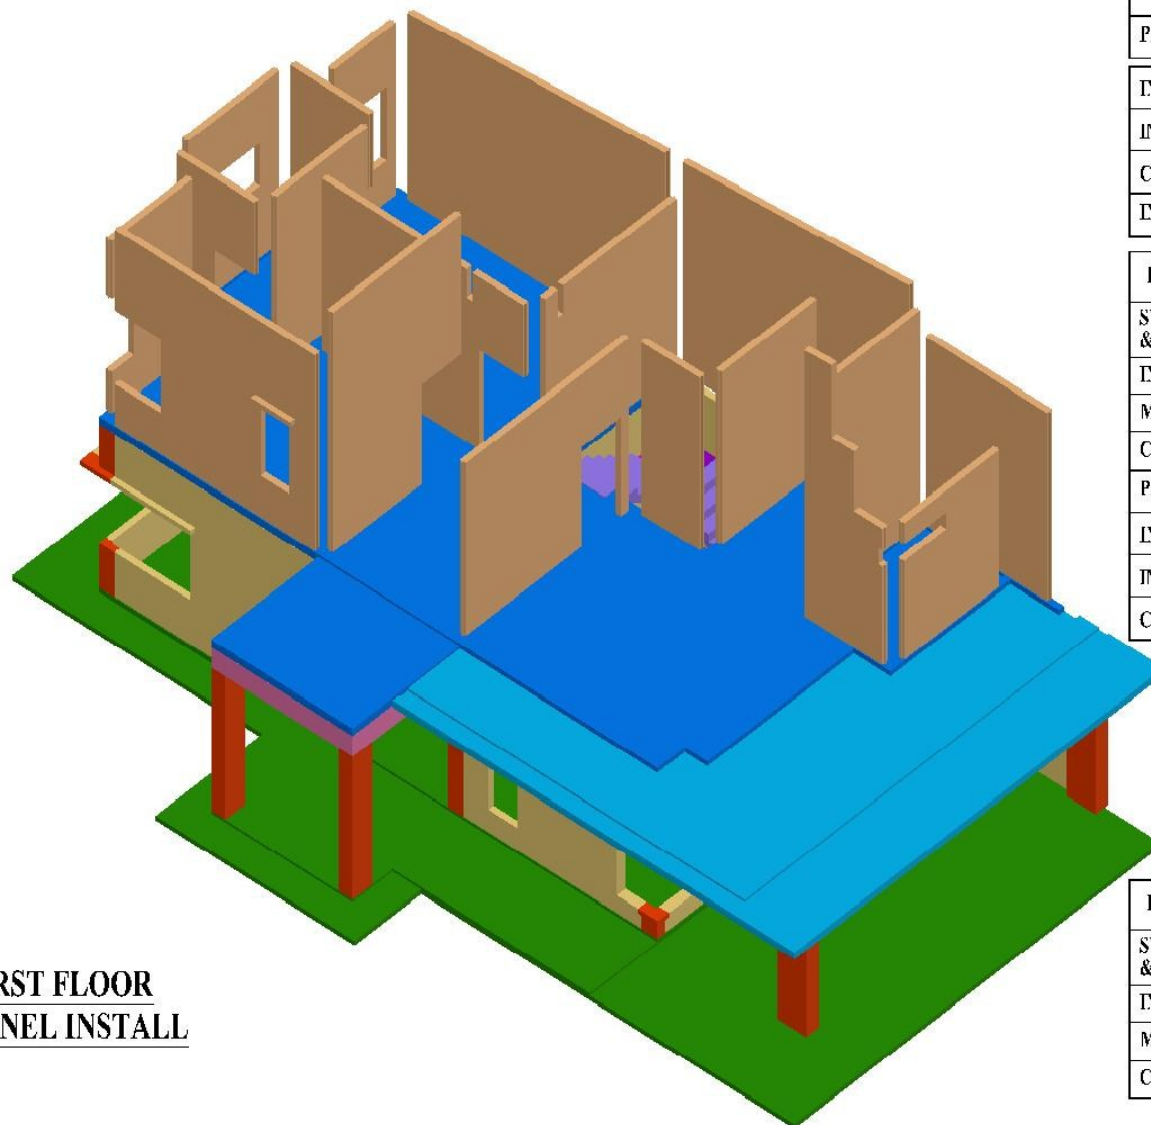


**FIRST FLOOR
PANEL INSTALL**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

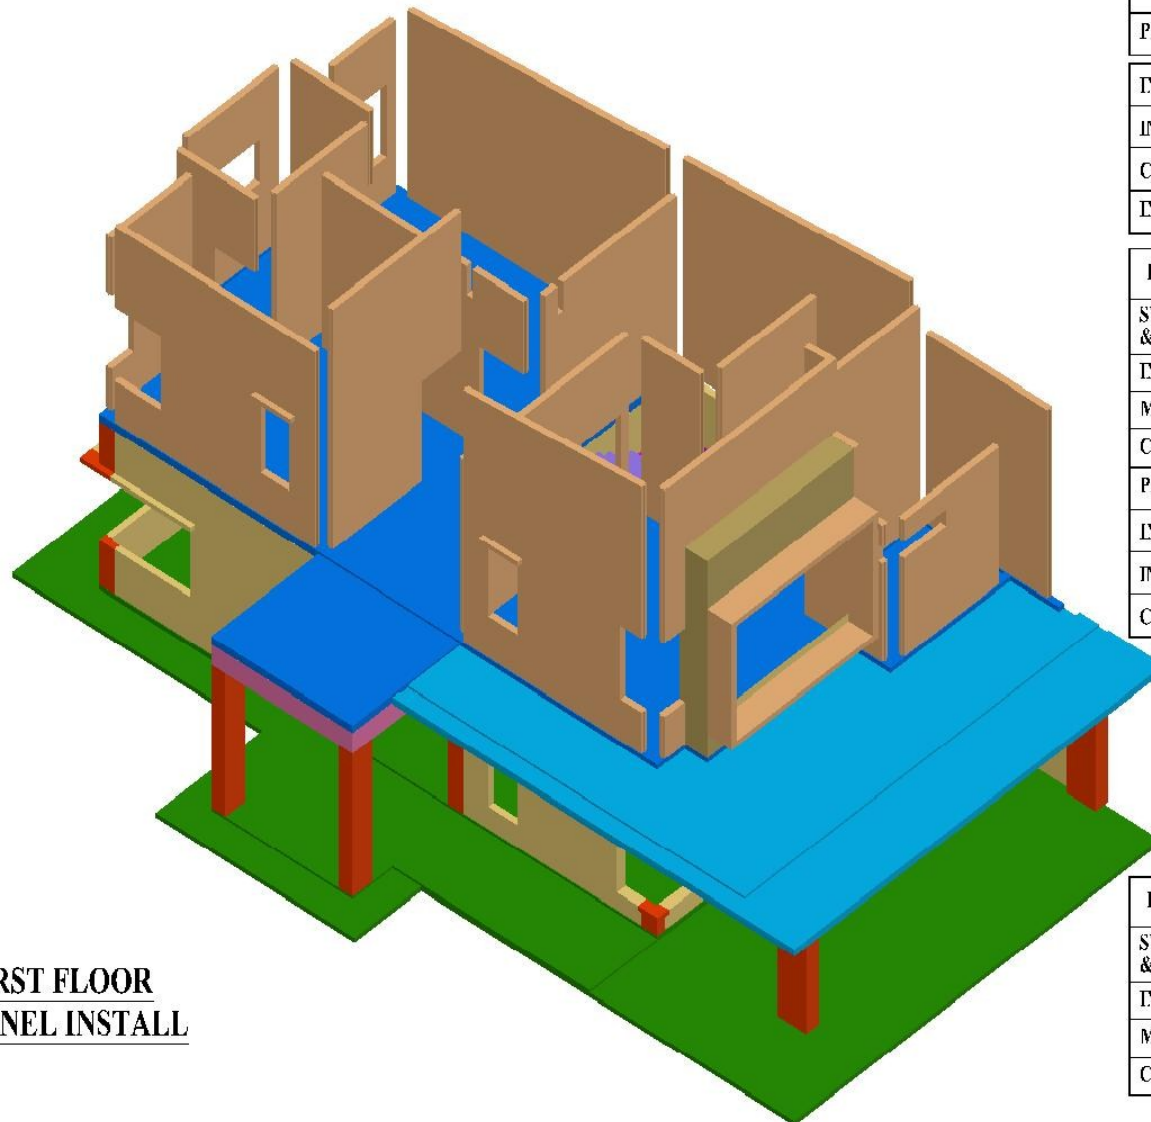


**FIRST FLOOR
PANEL INSTALL**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

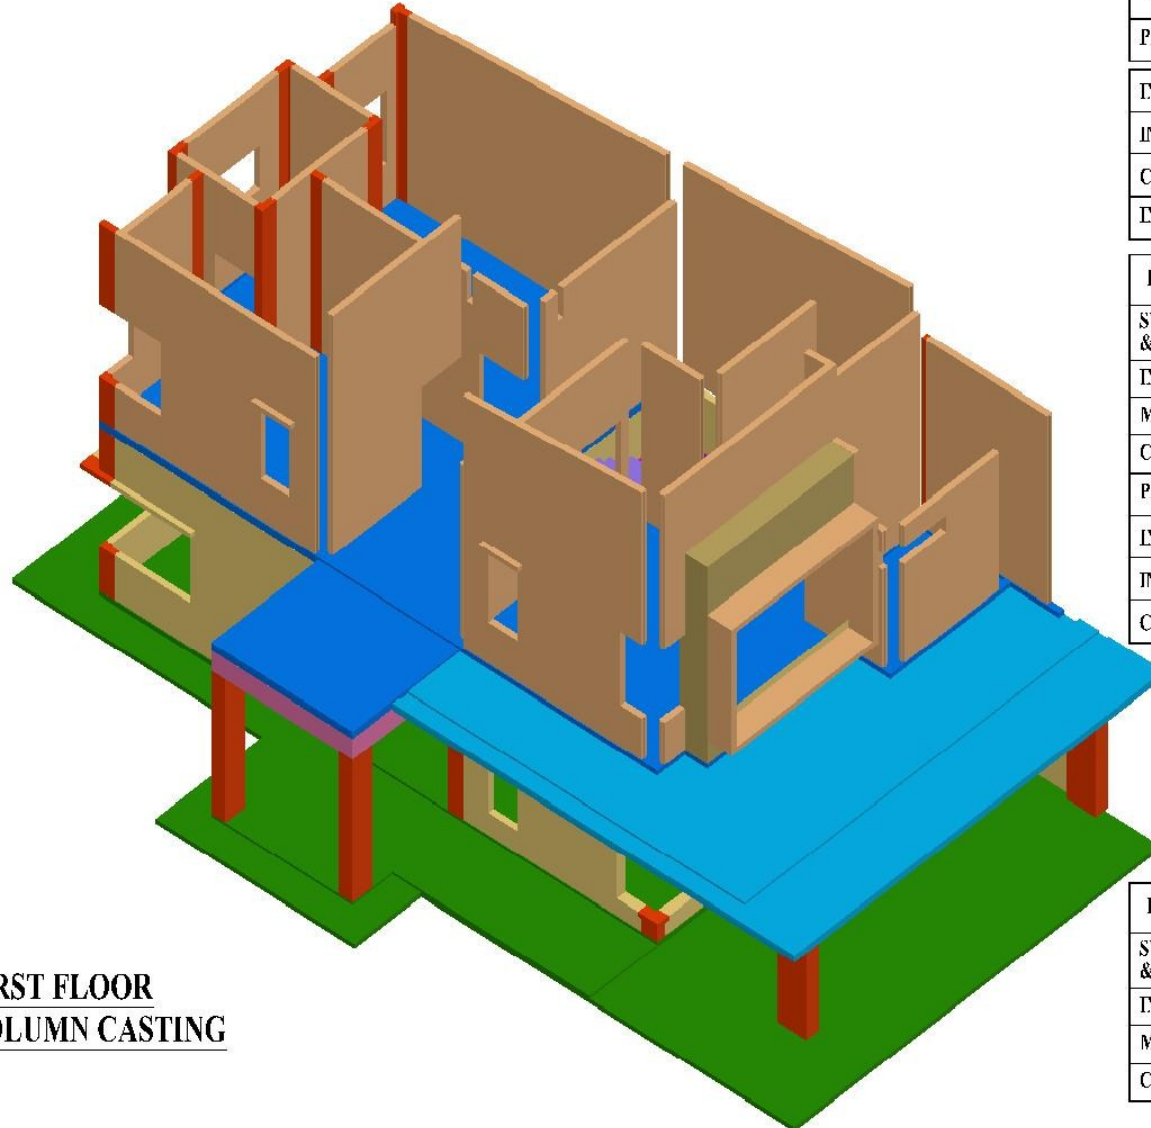


**FIRST FLOOR
COLUMN CASTING**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

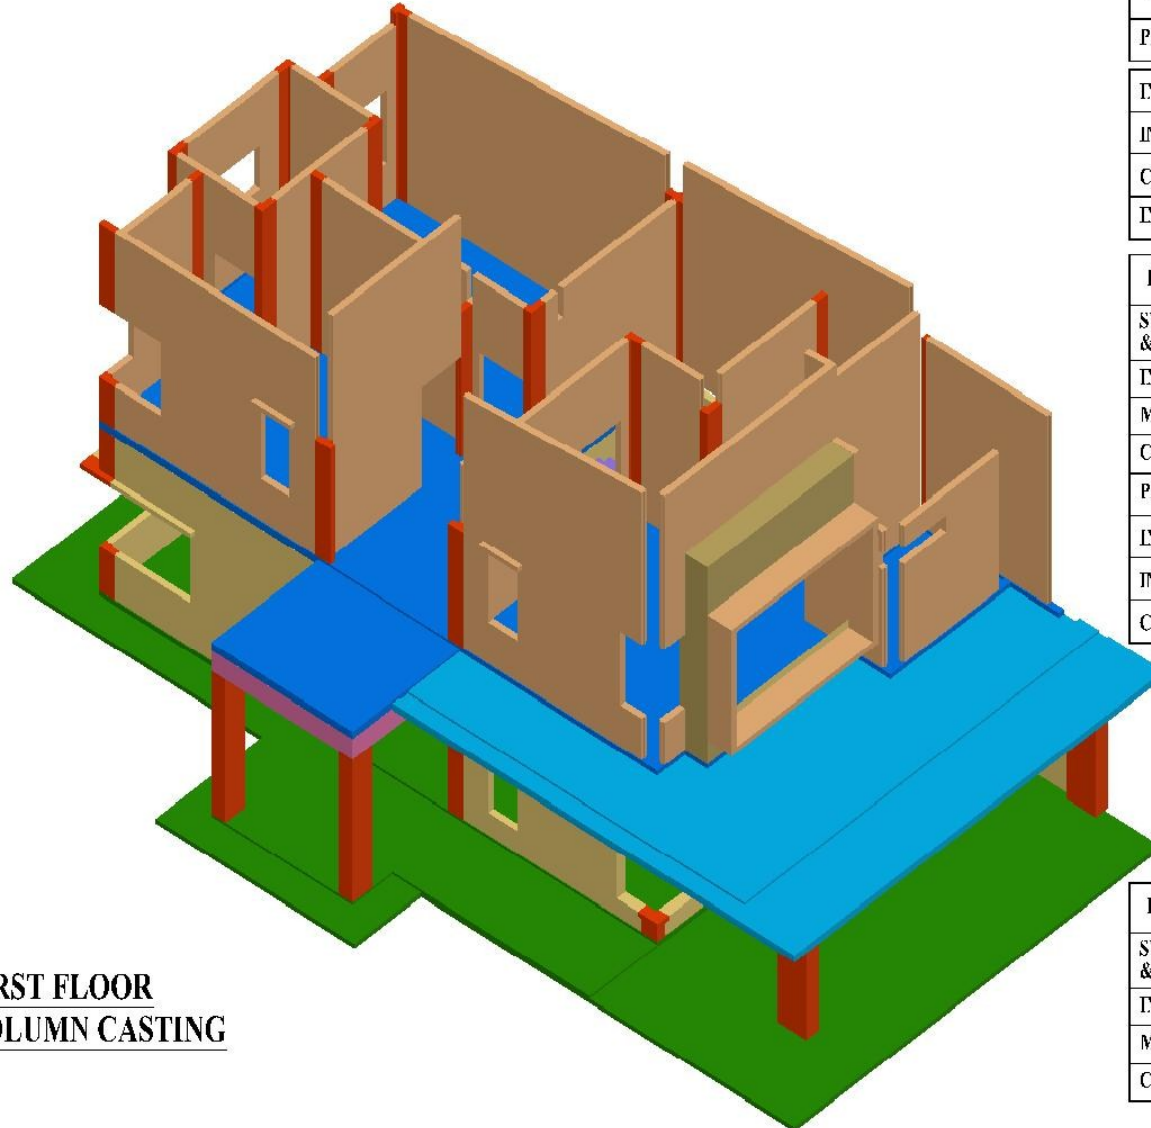


**FIRST FLOOR
COLUMN CASTING**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

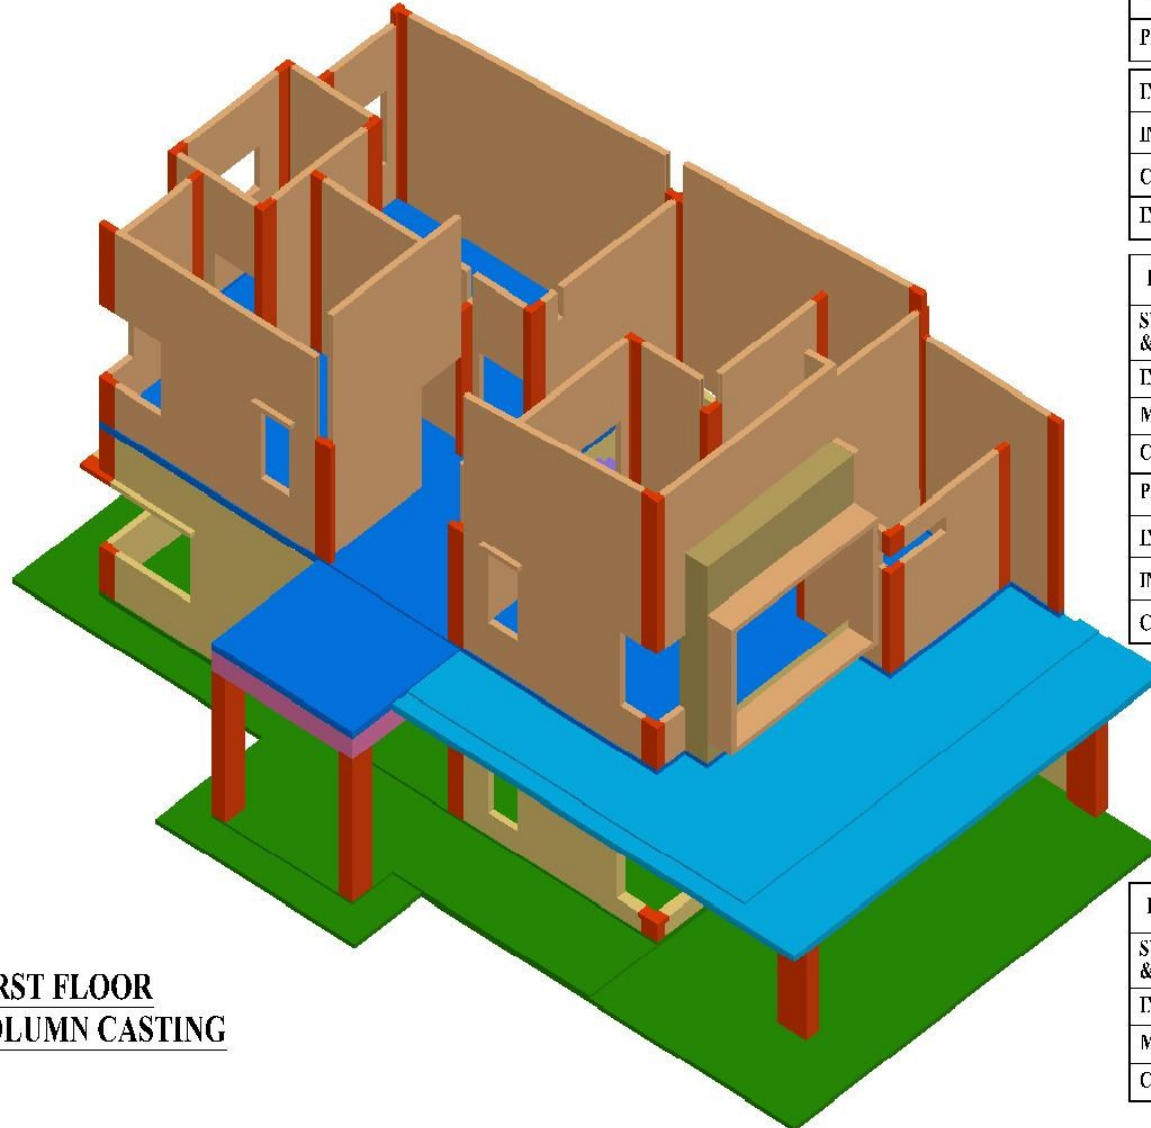


**FIRST FLOOR
COLUMN CASTING**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

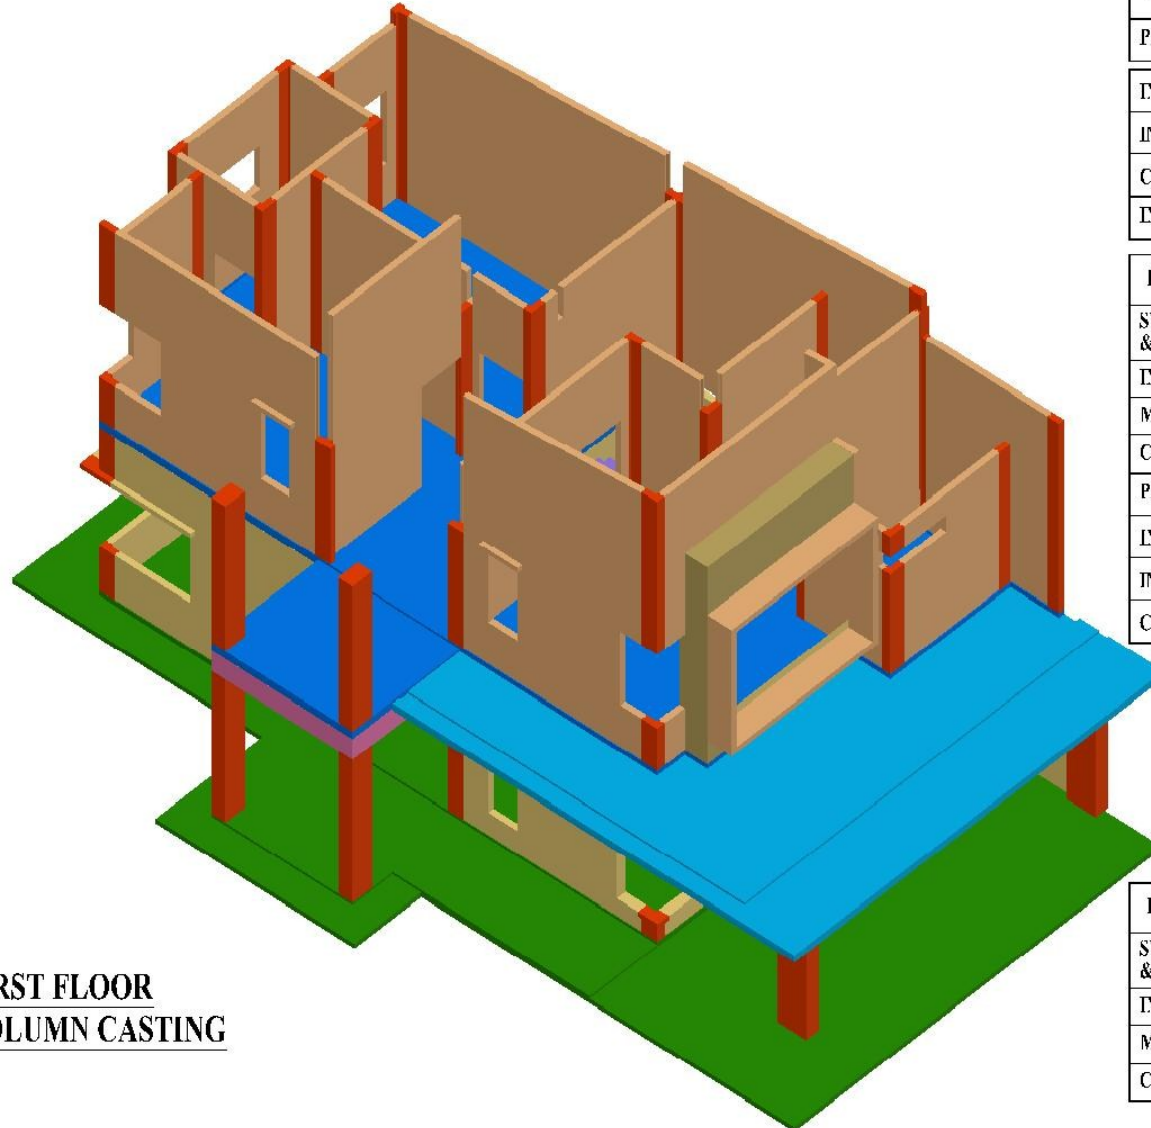


**FIRST FLOOR
COLUMN CASTING**

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

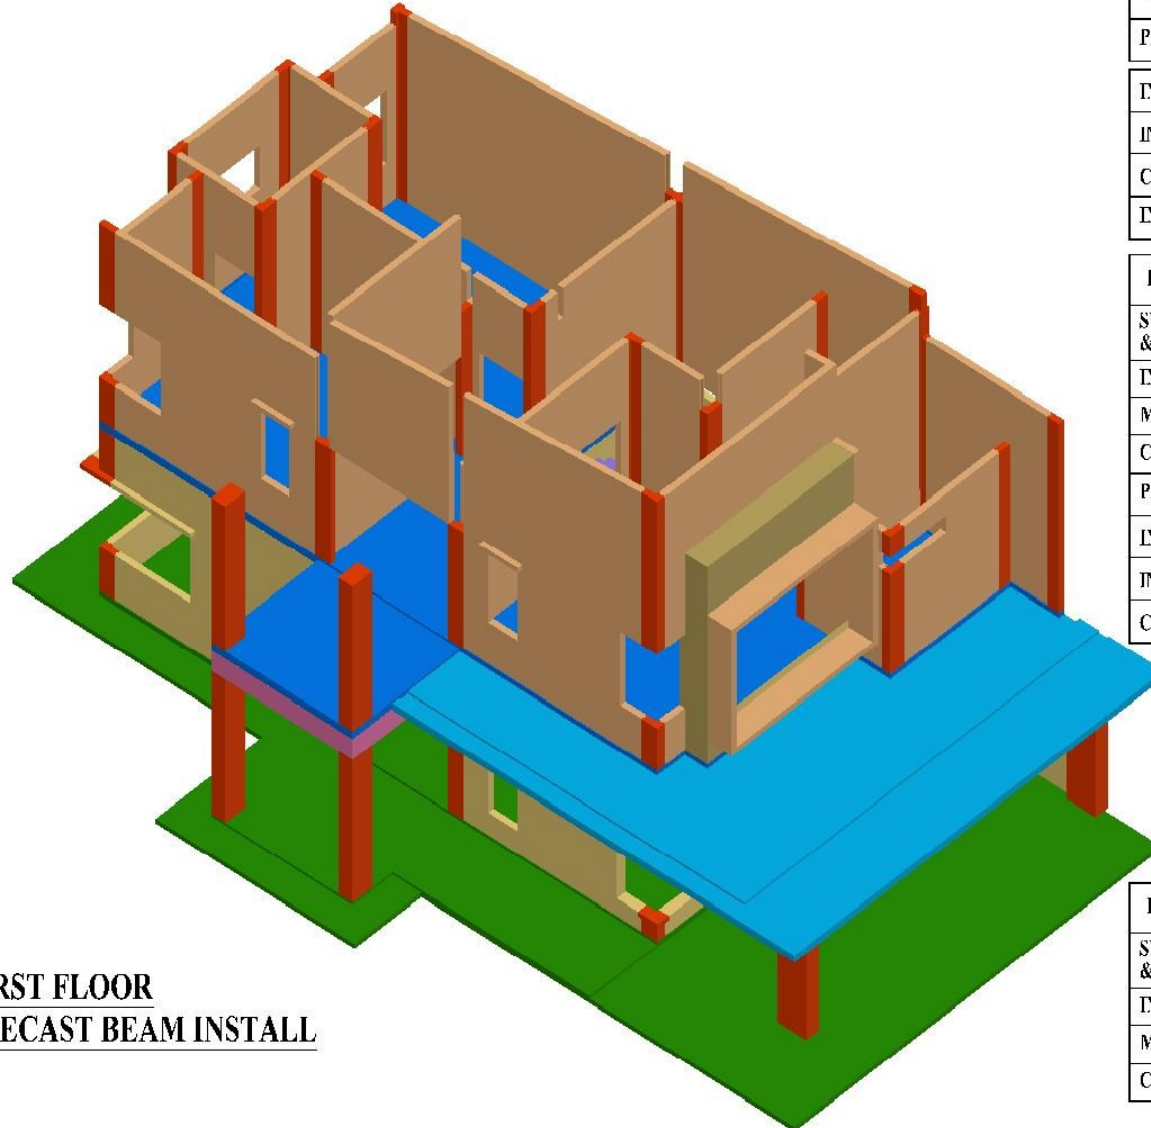


FIRST FLOOR
PRECAST BEAM INSTALL

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

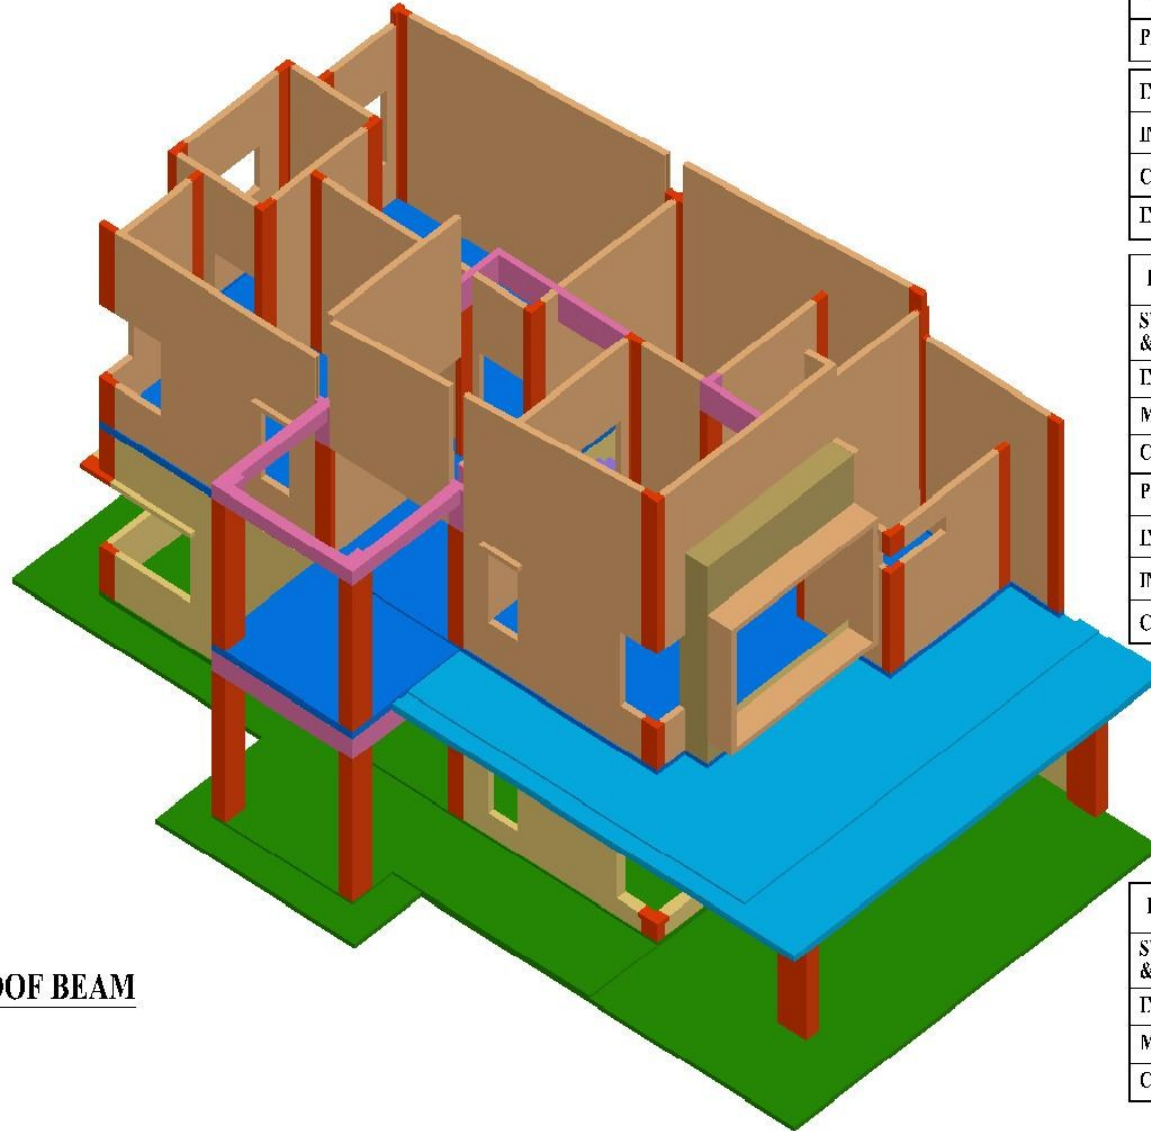


ROOF BEAM

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

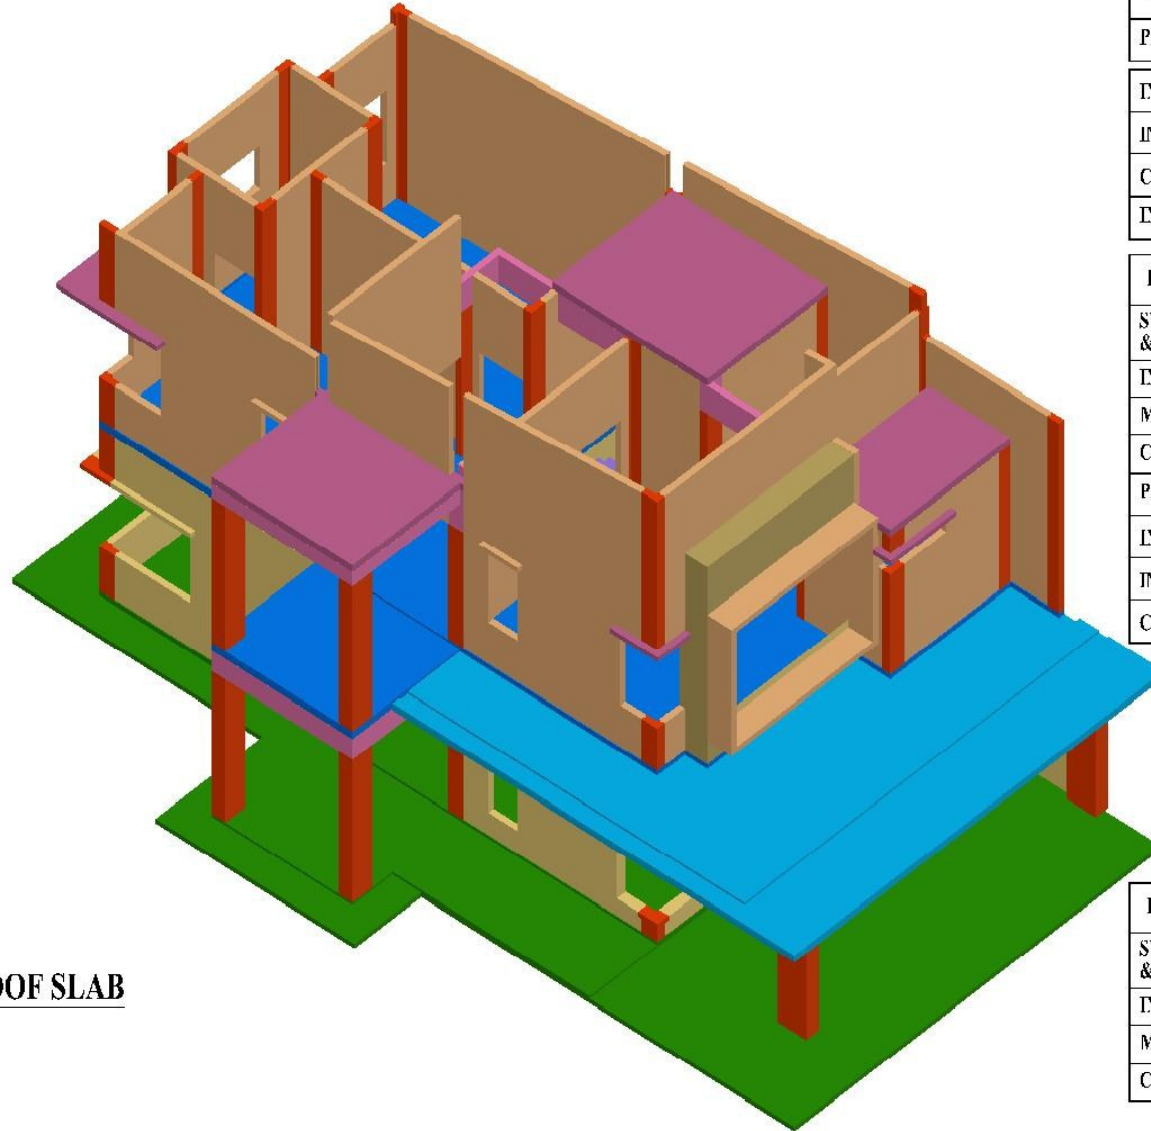


ROOF SLAB

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

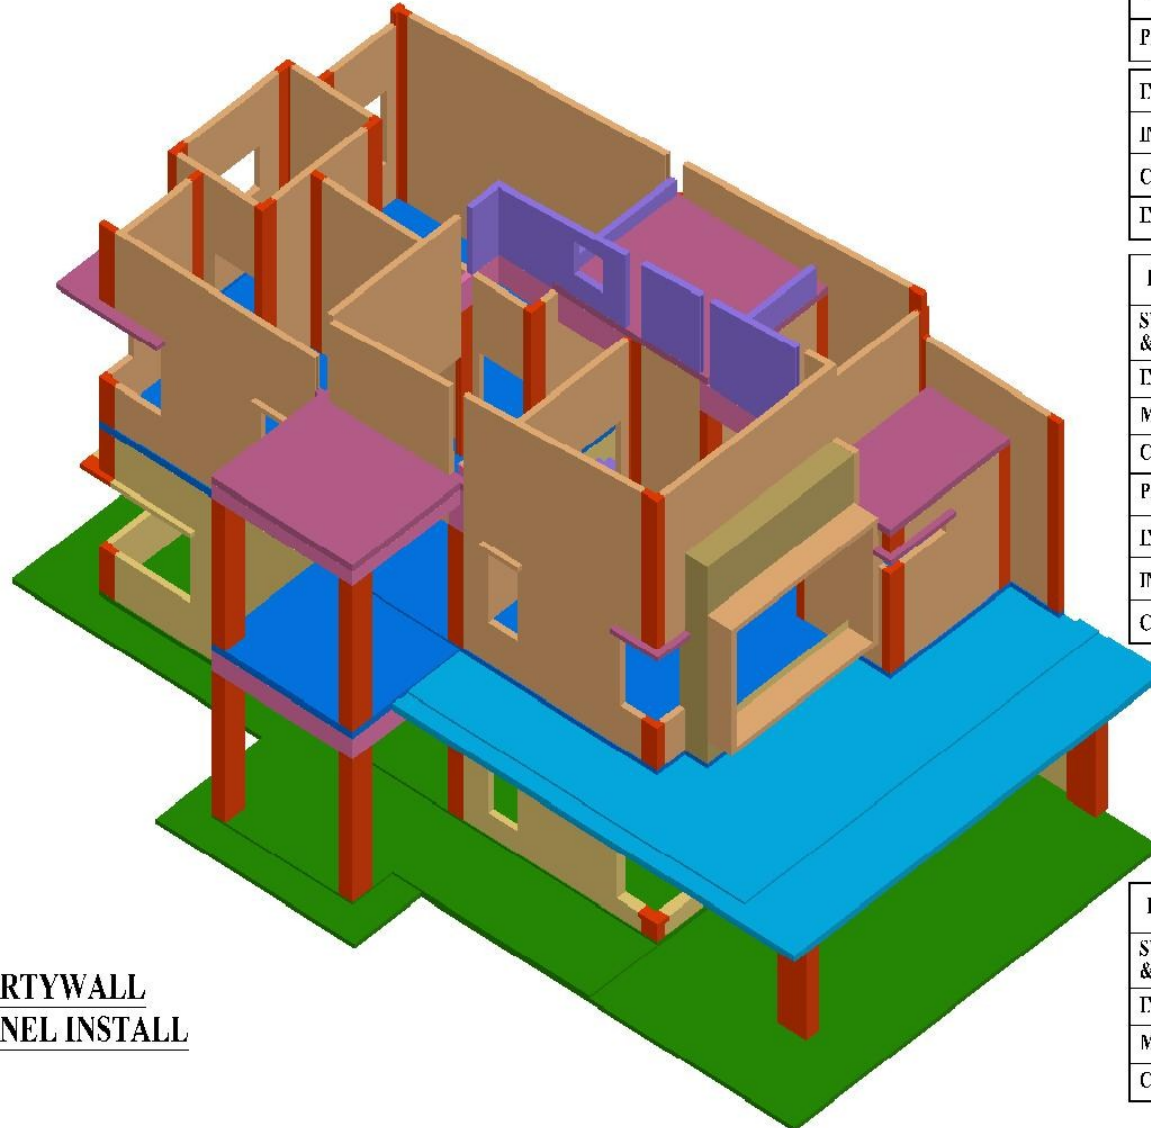


PARTYWALL PANEL INSTALL

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

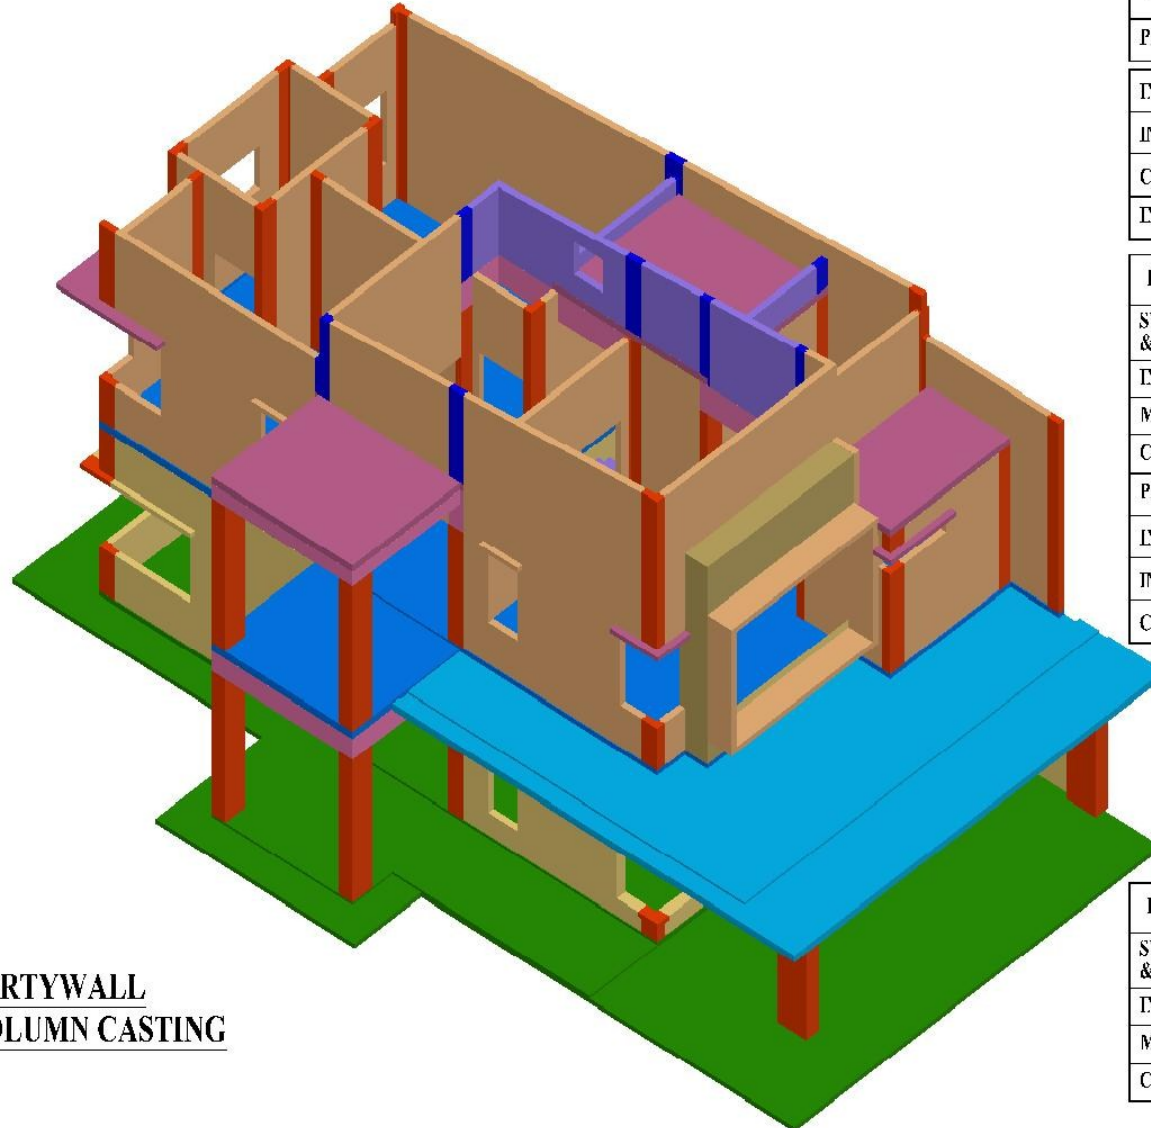


PARTYWALL COLUMN CASTING

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

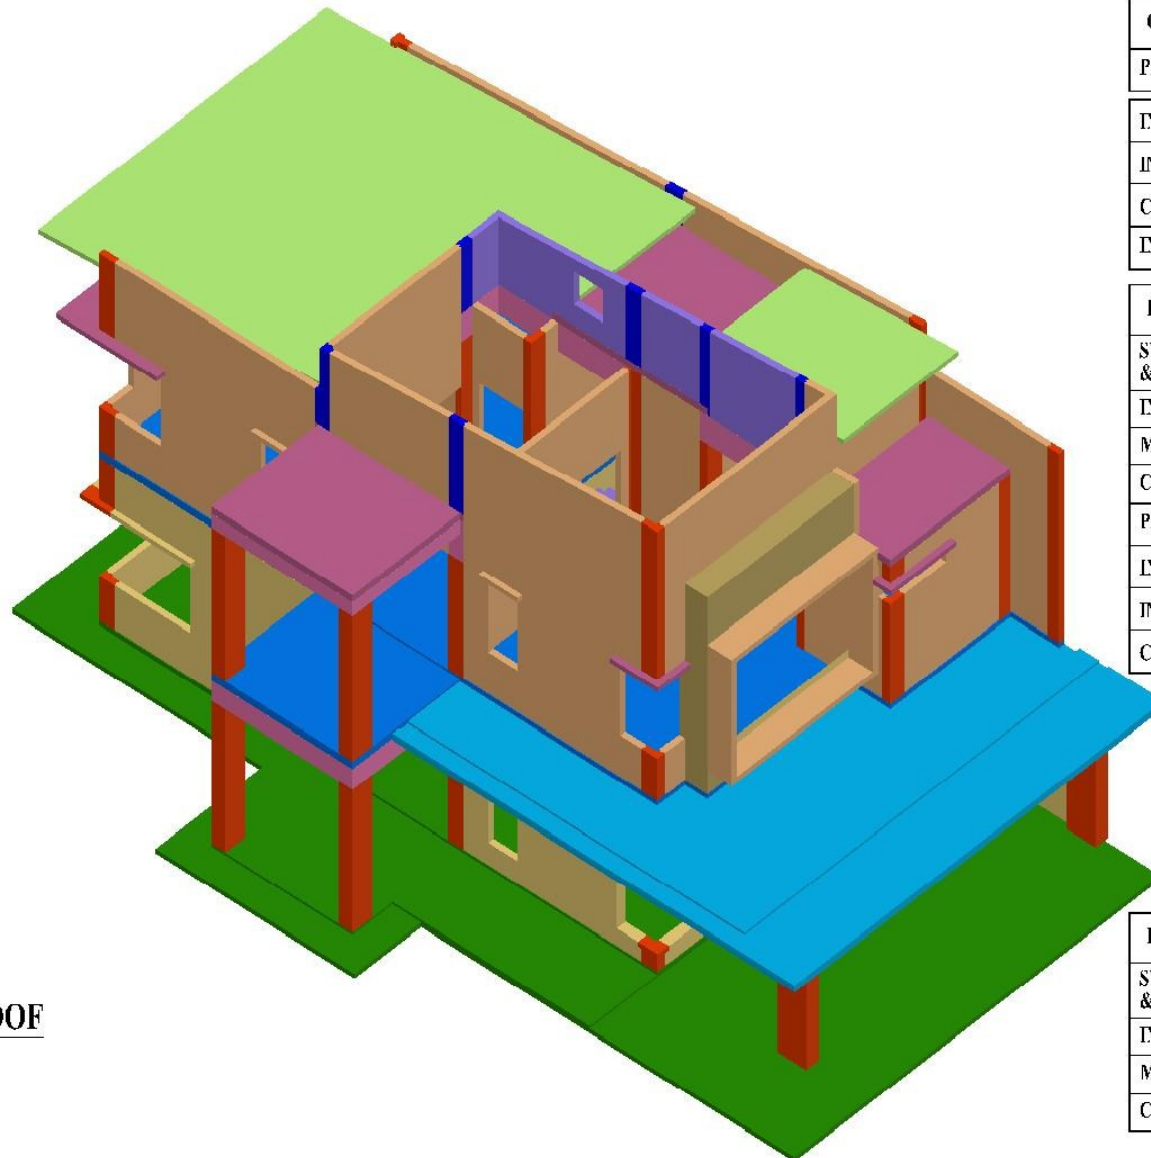


ROOF

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

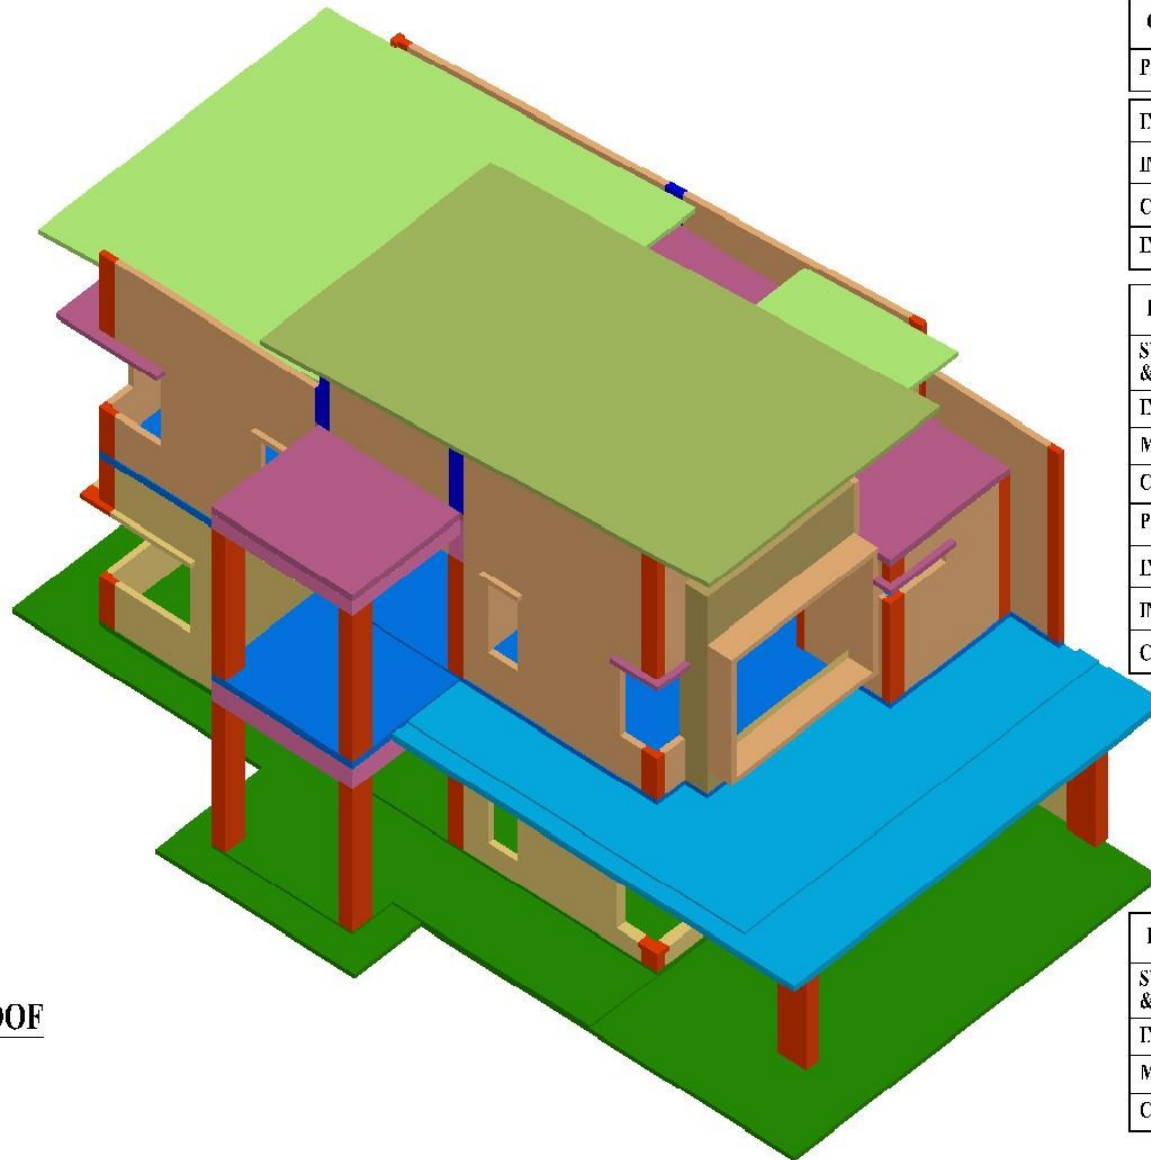

ROOF

GROUND FLOOR		25 tonne Mobile crane
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit
INSTALL STAIRCASE	WORKER (3+0)	Per Day 1 unit

FIRST FLOOR		25 tonne Mobile crane
SYSTEM BEAM MOULD & HALF SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit
PANEL INSTALLATION	WORKER (4+1)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
INSTALL COLUMN MOULD	WORKER (5+0)	Per Day 1 unit
CASTING COLUMN	WORKER (5+0)	Per Day 2 unit

ROOF		25 tonne Mobile crane
SYSTEM BEAM MOULD & SLAB SLAB	WORKER (5+0)	Per Day 1 unit
INSTALL REBAR	WORKER (5+0)	Per Day 1 unit
M&E SERVICES	WORKER (3+0)	Per Day 1 unit
CASTING BEAM & SLAB	WORKER (5+0)	Per Day 1 unit

DESIGNED BY YOU
PRODUCED BY
HC PRECAST SYSTEM
THANK YOU
